



BENTEN ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 11/28/2022-12/02/2022



Balfour Beatty

Current Activities 11/28/22-12/02/22


- Complete
 - Demolition of ceiling tile and grid
 - Removal of flooring and base
 - Removal of ductwork, fixtures, and equipment
- Started/Ongoing
 - Installing new mechanical ductwork
 - Electrical rough-in

Upcoming Activities 12/05/22-12/09/22

- Continue mechanical, electrical, and plumbing rough-in
- Layout new ceiling grid
- Layout of new VRF units




Ceilings & floors removed in the front hallway

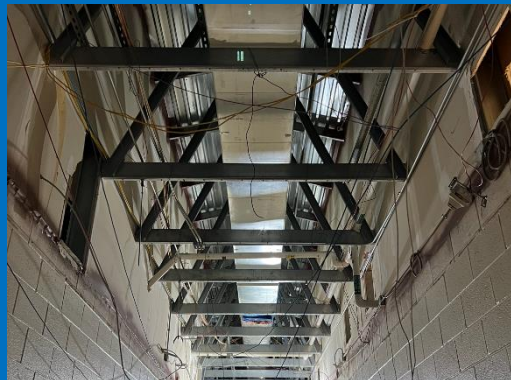

New Ductwork

Progress Photos

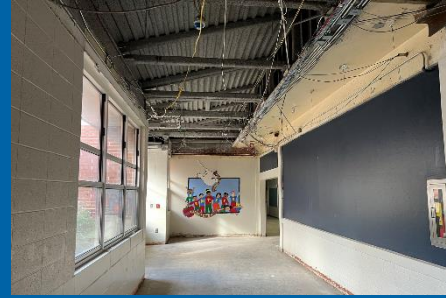

 **BRPH**

Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$1,027,541
- Budget Status: Within GMP

