

BENTEN

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 12/05/2022-12/09/2022



Balfour Beatty

Current Activities 12/05/22-12/09/22

- Complete
 - Demo of all ceiling tile, ceiling grid, flooring, and base
 - Removal of all mechanical, electrical, and plumbing equipment
- Started/Ongoing
 - Installing new ductwork
 - Hanging the new VRF cassette systems
 - Installing new overhead feeder conduit

Upcoming Activities 12/12/22-12/16/22



- Install indoor mechanical units
- Install mechanical piping
- Rough-in new conduit for new lighting



New Daikin VRF Cassette Systems



Progress Photos

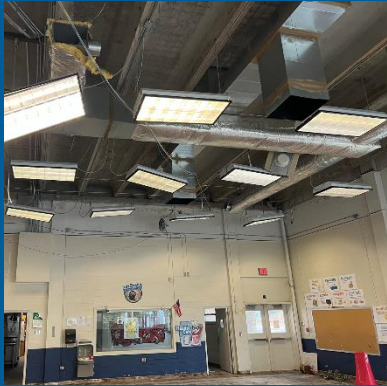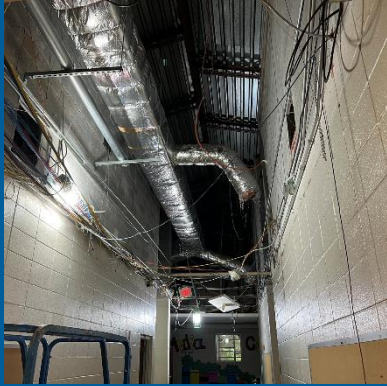

 **BRPH**

Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$1,027,541
- Budget Status: Within GMP

