

# BENTEEN

## ELEMENTARY SCHOOL

*Weekly Construction Progress Report*  
*Week 12/12/2022-12/16/2022*



**Balfour Beatty**

## Current Activities 12/12/22-12/16/22


- Complete
  - Demo of all ceiling tile, ceiling grid, flooring, and base
  - Removal of all mechanical, electrical, and plumbing equipment
- Started/Ongoing
  - Installing new ductwork
  - Hanging the new VRF cassette systems and associated piping
  - Installing new overhead feeder conduit for mechanical units and emergency lighting
  - Rough-in of conduit for lighting

## Upcoming Activities 12/19/22-12/23/22

- Install indoor mechanical units
- Cut block for new ductwork
- Rough-in conduit for lighting in Area D
- Testing and survey of existing exterior cameras
- Low voltage management of existing cabling
- Masonry block infill at unit wall ventilators



VRF cassette and electrical rough-in of unit at Gym Balcony

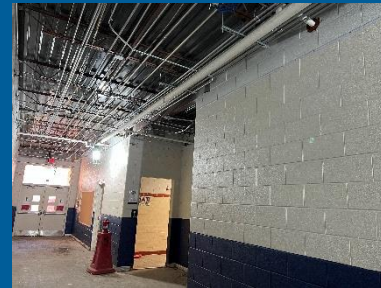

Rough-in of conduit for mechanical units and emergency lighting in Area C

## Progress Photos



Layout of new mechanical duct for holes to be cut in Area D



Delivery of roof insulation material and storage in lower parking lot



Posting of trees to be removed for Arborist Department signoff



Rough-in of VRF cassettes and conduit in Area B



Temporary plywood to secure locations where equipment was removed and prevent moisture intrusion



Water piping from previous air conditioning system removed from Area E

 **BRPH**

**Balfour Beatty**

## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$1,027,541
- Budget Status: Within GMP

