

BENTEEN

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 01/09/2023-01/13/2023



Balfour Beatty

Current Activities 01/09/23-01/13/23


- Complete
 - Cutting block for install of new ductwork
 - Masonry infill at unit wall ventilators
 - Selective demolition of casework
 - Demolition of marker and tack boards
 - Field measure for toilet partitions and roof steel
- Started/Ongoing
 - Hanging the new VRF cassette systems and associated piping
 - Installing new overhead feeder conduit for mechanical units and emergency lighting
 - Installation of spiral duct in Area A
 - Installation of duct in Area D

Upcoming Activities 01/16/23-01/20/23

- Install linesets and drains at VRF cassettes
- Ceiling work in restrooms
- Install fire dampers and round pipes in Area B
- Low voltage management of existing cabling
- Pulling of electrical wire in Areas B and C
- Install of intercom and communication wiring



CMU infill complete at Area D

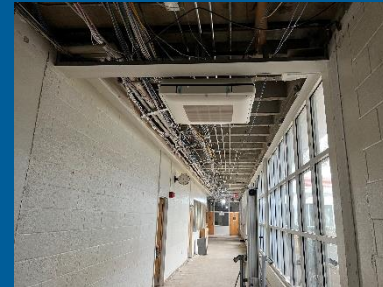

Installation of VRF cassette unit in front hallway

Progress Photos



Coring of holes for ductwork in Area E



Linesets connected to VRF cassettes in Area C



Installation of spiral duct in Area A



Linesets connected to VRF cassettes in Media Center



Disposal of remaining markerboards and tackboards



Installation of emergency lighting conduit in Area E

 BRPH

Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$2,335,159
- Budget Status: Within GMP

