

# BENTEN

## ELEMENTARY SCHOOL

*Weekly Construction Progress Report*  
*Week 01/30/2023-02/03/2023*




**Balfour Beatty**

## Current Activities 01/30/23-02/03/23

- Installation of VRF line sets and cassettes at areas D and E.
- Installation of Fire Dampers at area D.
- Electrical rough-in for emergency life safety system.
- Installation of electrical shut off switches for VRF system at area D and E.
- Installation of hard ceilings and patching at restrooms in area A and B.
- Demolition and installation of new TPO roofing at Kitchen completed.
- Shrubs Demolished at front entry completed.
- Abatement at boiler room completed
- Prep and prime corridor walls in area B & C
- Loading roof at area D for new TPO roofing installation

## Upcoming Activities 02/06/23-02/10/23

- Selective demolition for secure entry vestibule
- Installation of equipment curbs on roof @ Area D
- Wall preparation for paint throughout the building
- Demolition and installation of new TPO roofing at area D.
- Demolition of front entry sidewalk and doors/windows
- Prep restroom floors to receive new epoxy flooring
- Installation of rooftop equipment support steel.
- Damp proofing of CMU infills

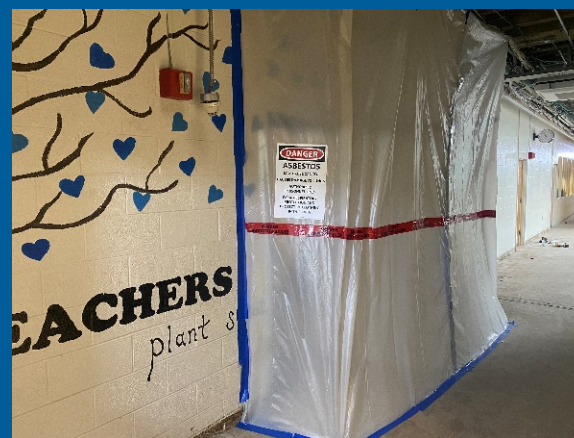

Exclusion zone for abatement work



Shrubs demolished at front entry

 **BRPH**

**Balfour Beatty**

## Progress Photos



Exclusion Zone for abatement work



Loading roofing material onto roof @  
Area D



Rough-in for main electrical lines in Area D



Installment of Adjustastair for roof access



Loading and Installing warning lines @  
Area D Roof

## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$2,335,159
- Budget Status: Within GMP



**Balfour Beatty**
