

BENTEN

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 02/20/2023-02/24/2023




Balfour Beatty

Current Activities 02/20/23-02/24/23

- Installation of VRF line sets and cassettes at areas D and E.
- Installation of electrical shut off switches for VRF system at area D and E.
- Demolition and installation of new TPO roofing at D-East
- Installation of equipment curbs on roof @ Area D
- Wall preparation for paint throughout the building
- Installation of rooftop equipment support steel at area D.
- Installing epoxy on restroom floors area A, B, C
- Excavation of secure vestibule and canopy footings - Completed
- VRF Line set pressure testing – ongoing
- Insulation of duct work at area B, and C
- Pouring of S.O.G and canopy footings - Completed
- Insulation of duct work at area B, and C
- Install ceiling grid in Area A, B, and C
- Electrical Equipment Pads being poured

Upcoming Activities 02/27/23-03/03/23

- Damp proofing of CMU infills
- Rooftop steel at cafeteria installation at area E
- Install Bathroom Fixtures
- Install Lights & low volt in ceiling grid in area A, B, C
- Prep Exterior equipment pads

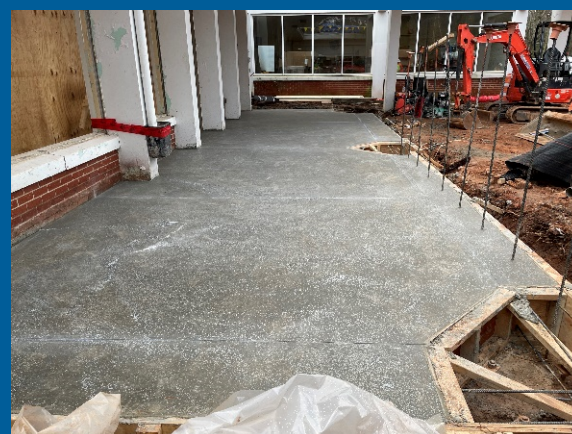

Vestibule Slab-on Grade Poured




Metal Canopy footings being poured

 **BRPH**

Balfour Beatty

Progress Photos

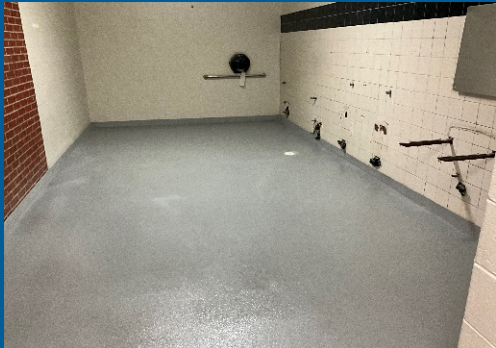


Epoxy on Restroom Floors Area A,C



Ceiling Grids Install at Area B, C



Gym Mezzanine New Handrail Paint

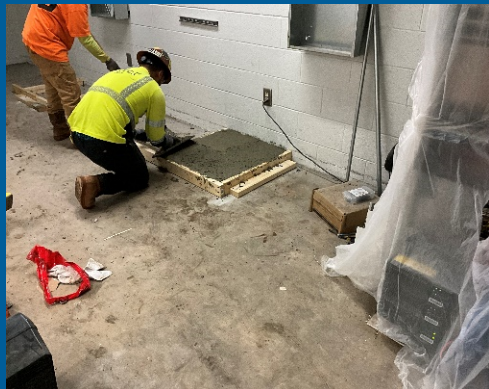

Finishing of Electrical Equipment Pad



Main-Electrical Line Rough-in with pull
can

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$3,154,691
- Budget Status: Within GMP



Balfour Beatty
