

BENTEN

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 03/20/2023-03/24/2023



Balfour Beatty

Current Activities 03/20/23-03/24/23

- Installation of VRF line sets and cassettes at areas D and E.
- Installation of electrical shut off switches for VRF system at area D and E.
- Demolition and installation of new TPO roofing at D-East/D-West
- Installation of equipment curbs on roof @ Area E - Complete
- Wall preparation for paint throughout the building
- Installing epoxy on restroom floors Area D-West - Ongoing
- VRF Line set pressure testing – ongoing
- Prepping Floor for Epoxy in Area E - Ongoing
- Installation of low voltage data drops in Area A,B,C
- Rooftop steel at cafeteria installation at area E - Completed
- Install Bathroom Fixtures – Ongoing
- Install Lights & low volt in ceiling grid in area A, B, C
- Install Vestibule Steel in front entry area - Complete
- Insulation of Ductwork In Area E - Ongoing
- Install Corridor Lights – Ongoing
- CMU Infills brick laid - Ongoing
- Courtyard Mulching - Ongoing

Upcoming Activities 03/27/23-03/31/23

- Paint Bathroom Ceilings
- Install ceiling grid in Area D-East/West
- Install Toilet Partitions
- CMU Infills brick laid
- Cut Ceiling Tile Border
- Run Pipe for Generator
- Restroom Ceiling Work



Vestibule Steel Decking Installed



Courtyard Mulch Laid

Progress Photos



Main electrical feeders for new panels installed



Trenching for LED Monument Sign Ongoing



Brick infills completed




HVAC Rooftop Curbs Set and walkway pads installed at Area D-East roof



Replacement/New Casework delivered to site

Roofing Progress Photos

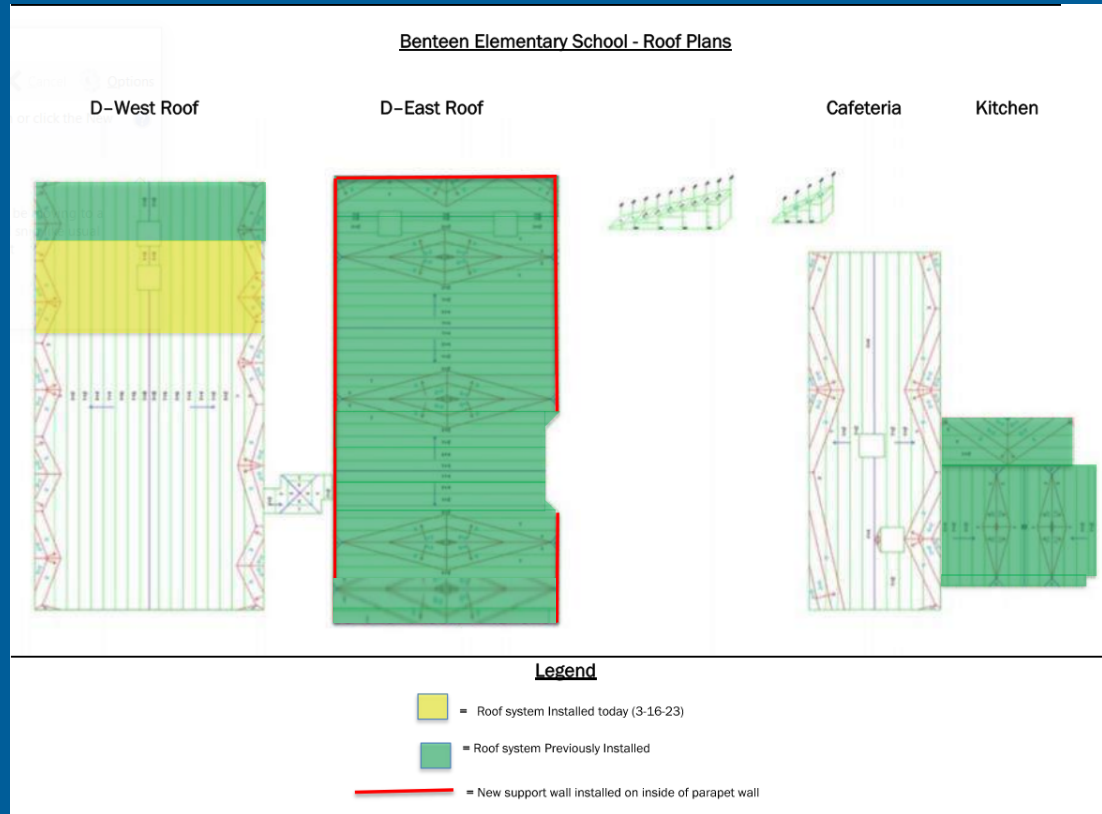

 **BRPH**

Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$3,154,691
- Budget Status: Within GMP



Balfour Beatty
