

BENTEN

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 04/10/2023-04/14/2023



Balfour Beatty

Current Activities 04/10/23-04/14/23

- Installation of VRF line sets and cassettes at areas D and E.
- Installation of electrical shut off switches for VRF system at area D and E.
- Wall preparation for paint throughout the building
- Prepping Floor for Epoxy in Area E - Ongoing
- Installation of low voltage data drops in Area A,B,C
- Install Bathroom Fixtures – Ongoing
- Install Lights & low volt in ceiling grid in area A, B, C
- Insulation of Ductwork In Area E - Ongoing
- Install Corridor Lights – Ongoing
- CMU Infills brick laid - Ongoing
- Courtyard Mulching – Ongoing
- Install ceiling grid in Area D-East/West
- CMU Infills brick laid
- Cut Ceiling Tile Border
- Run Pipe for Generator
- Restroom Ceiling Work
- Install Toilet Partitions
- Mechanical Pad concrete pour
- Vestibule Diamonds pour backs

Upcoming Activities 04/17/23-04/21/23

- Paint Bathroom Ceilings
- Restroom Ceiling Work
- Stub line-sets through roof
- Mechanical Ceiling cover-up inspection
- Concrete footing pour at sign and screen-wall
- Install Decking for Metal Canopy
- Install brick and cast stone around canopy post



 **BRPH**



Crane Mobilized for Rooftop HVAC Units




Canopy Columns Erected

Balfour Beatty

Progress Photos



HVAC unit pad being formed for concrete
Pour

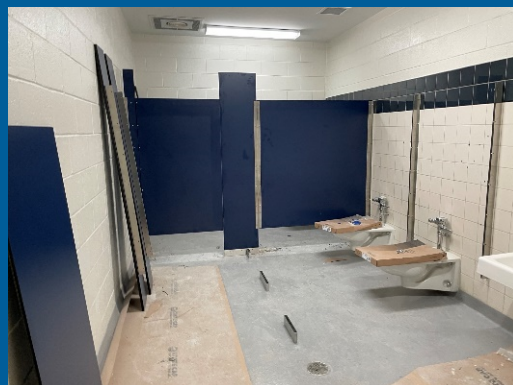

Toilet Partition Install in Restrooms



West Courtyard Drainage Pipe Replacement



Rooftop HVAC units landed on roof



New 600AMP Breaker Installed

 **BRPH**

Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$4,262,671
- Budget Status: Within GMP



Balfour Beatty
