

BENTEN

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 04/24/2023-04/28/2023



Balfour Beatty

Current Activities 04/24/23-04/28/23

- Installation of electrical shut off switches for VRF system at area D and E.
- Wall preparation for paint throughout the building - Complete
- Prepping Floor for Epoxy in Area E - Ongoing
- Installation of low voltage data drops in Area A,B,C
- Install Bathroom Fixtures – Ongoing
- Install Lights & low volt in ceiling grid in area A, B, C
- Insulation of Ductwork In Area E - Ongoing
- Install Corridor Lights – Ongoing
- Courtyard Mulching – Complete
- Install ceiling grid in Area D-East/West - Complete
- Cut Ceiling Tile Border
- Install Toilet Partitions - Ongoing
- Concrete footing pour at sign and screen-wall - Complete
- Install Decking for Metal Canopy - Complete
- Install brick and cast stone around canopy post - Complete

Upcoming Activities 05/01/23-05/05/23

- Paint Bathroom Ceilings
- Stub line-sets through roof
- Install Brick at HVAC enclosure
- Install Gas line on roof
- Offsite Planting
- Install Ceiling Tile in Area A
- Room 1110 Drywall Install
- Final Coat of Finish Paint
- Vestibule Framing



Security Vestibule Brick & Cast stone wall installed



Brick and Cast stone canopy columns installed

Progress Photos




Devices being installed into ceiling tile



Kiln Hood and Ductwork installed



Kitchen Epoxy being installed

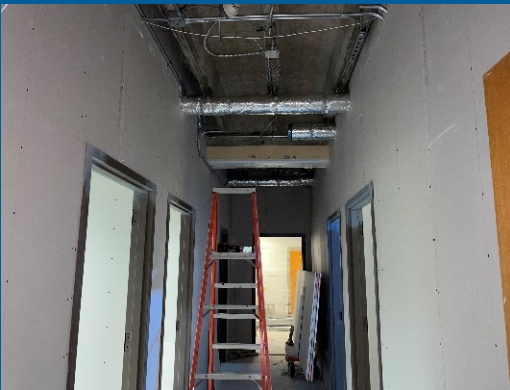

Drywall/Insulation installed in New Office/conference room area



L.E.D Monument sign CMU and Brick Installation Ongoing

BRPH

Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$4,262,671
- Budget Status: Within GMP



Balfour Beatty
