

BENTEN

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 06/19/2023-06/23/2023



Balfour Beatty

Current Activities 06/19/2023-06/23/2023

- Fire Alarm Testing and Troubleshooting – Ongoing
- Owner / Architect / Engineer Punch walk
- Move-in Classroom Furniture - Ongoing
- Electrical Final Inspection - Completed
- Air Handling Units Install - Ongoing
- Install Fencing – Outside Air Units
- Install Kitchen Equipment
- Wax stage – Area A



Wax Gymnasium's Stage



Classroom Furniture currently moving in

Upcoming Activities 06/26/23-06/30/23

- Install River rock gravel around ground HVAC Units
- Mechanical and Plumbing Final Inspections
- Rooftop HVAC start-up
- Paint Gas Line

Progress Photos



Install Air Handling Unit in the Gym




New Classroom Furniture Setup Prep



New Classroom furniture delivery



Install Fencing for Outside Air Units

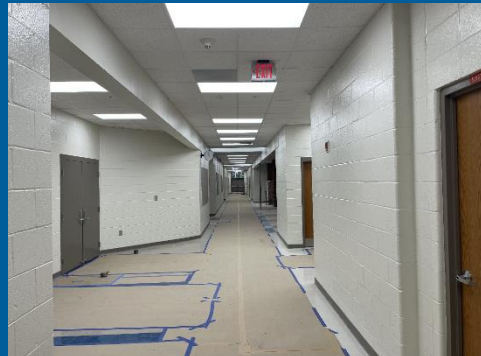

Floor Protection for Furniture Installation



Installation of Kitchen Equipment

 **BRPH**

Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$9,989,727.77
- Progress Billed to Date: \$7,734,405.60
- Budget Status: Within GMP

