

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

April 2, 2020

Prepared For: Atlanta Public Schools

Prepared By: Seth Nama



New Addition Ceiling Grid



Media Center Lights




Site Demo At Main Entrance



South Elevation GAB



Drywall in STEM Lab

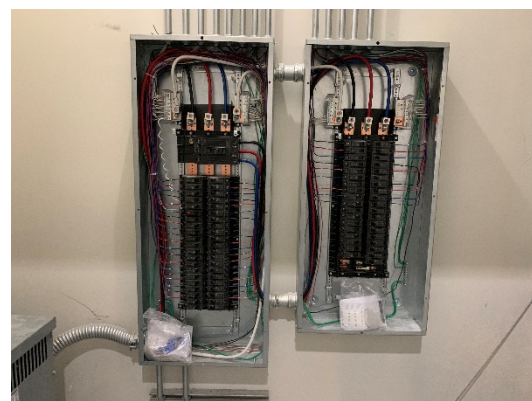

Breaker Box In New Addition

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

April 2, 2020



Last Week's Activities:

- Continued final coat of paint in buildings 2033 & 2040
- Continued VCT floor installation in buildings 2033 & 2040
- Continued brick staining
- Completed exterior precast tile installation
- Began installing canopies
- Continued installing storefront at main entrance
- Completed epoxy flooring in stairwells
- Completed curb and gutter installation at South elevation
- Completed replacing low roof
- Continued installing canopy footings
- Continued media center paint

This Week's Activities:

- Continued VCT floor installation in buildings 2033 & 2040
- Continued brick staining
- Continued installing storefront at main entrance
- Began existing front entry site demo
- Began ceiling grid installation in new addition
- Completed South elevation GAB installation
- Continued installing canopy footings
- Began installing metal coping
- Began priming in new addition

Next Week's Activities:

- Complete brick staining
- Complete VCT floor installation in buildings 2033 and 2040
- Complete storefront installation at main entrance
- Continue East hardscapes
- Begin replacing roof gutters
- Complete media center paint
- Complete canopy footings at South elevation
- Continue existing front entry demo
- Complete ceiling grid installation in new addition
- Begin door installation
- Begin ACM metal panel installation at new addition

Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$6,100,009
