

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

April 9, 2020

Prepared For: Atlanta Public Schools

Prepared By: Seth Nama



South Elevation Canopy Footing



West Elevation Roof Gutters




Front Entry Grading



Paint At New Addition



Interior Storefront Entrance

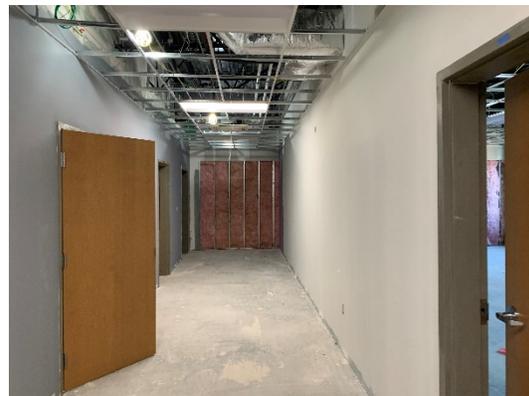

Doors At New Addition

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

April 9, 2020



Last Week's Activities:

- Continued VCT floor installation in buildings 2033 & 2040
- Continued brick staining
- Continued installing storefront at main entrance
- Began existing front entry site demo
- Began ceiling grid installation in new addition
- Completed South elevation GAB installation
- Continued installing canopy footings
- Began installing metal coping
- Began priming in new addition

This Week's Activities:

- Continued brick staining
- Continued installing storefront at main entrance
- Completed existing front entry site demo
- Completed ceiling grid installation in new addition
- Began bathroom tile installation in new addition
- Completed installation of South canopy footings
- Continued installing metal coping
- Began first coat of paint in new addition
- Began replacing roof gutters
- Began door installation

Next Week's Activities:

- Continue brick staining
- Complete VCT floor installation in buildings 2033 and 2040
- Complete storefront installation at main entrance
- Begin wood flooring installation in media center
- Complete East hardscapes
- Continue replacing roof gutters
- Begin canopy footings at East elevation
- Continue door installation
- Begin ACM metal panel installation at new addition
- Begin curb and gutter at East elevation
- Begin gym flooring

Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$6,100,009
