

**WEEKLY CONSTRUCTION PROGRESS
REPORT**
Humphries Elementary School
June 4, 2020

Prepared For: Atlanta Public Schools

Prepared By: Seth Nama



Media Center Carpet



South Elevation Pavement




Loose Furnishings



Stained Concrete



Concrete At The Main Entrance

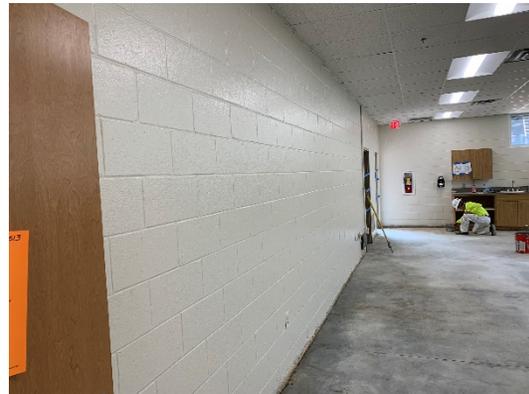

Final Coat of Paint in Building 2050

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

June 4, 2020



Last Week's Activities:

- Continued door installation
- Completed sidewalk installation at South & West elevations
- Completed prime/ first coat of paint in building 2031
- Began final coat of paint in building 2031
- Completed final coat of paint in the new addition
- Completed casework installation in buildings 2033 and 2040
- Continued prime/ first coat of paint in building 2050
- Completed installation of roof gutters on building 2032
- Began paving at the South elevation
- Completed interior signage installation

This Week's Activities:

- Continued door installation
- Completed sidewalk installation at East elevation
- Began final coat of paint in building 2050
- Completed casework installation
- Completed prime/ first coat of paint in building 2050
- Completed paving at the South elevation
- Began carpet tile flooring installation in building 2031
- Completed carpet tile flooring installation in building 2050
- Completed final coat of paint in buildings 2033, 2040, and 2031

Next Week's Activities:

- Complete door installation
- Complete final coat of paint in building 2050
- Complete carpet tile flooring installation in building 2031
- Complete all concrete
- Complete paving at the East elevation
- Complete flagpole installation
- Complete landscape installation

Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$8,427,779
