

# WEEKLY CONSTRUCTION PROGRESS REPORT

---

**Project: Howard Middle School**  
**Week Ending: July 20, 2018**

## **THIS WEEK:**

- OAC Meeting on July 18<sup>th</sup>
  - Discussing Phase 2 permit comments
- Erection of scaffolding continuing
- Layout for sub floor plumbing continuing
- Electricians continuing to wire temporary lighting/outlets
- Sitework grading beginning
- Saw cutting for plumbing trenches beginning
- Brick anchors being installed
- Bid Day for Phase 2 on July 17

## **NEXT WEEK – July 23 thru 27:**

- Masonry Restoration scaffolding continuing.
- OAC Meeting 07/25
- Masonry Restoration subcontractor continuing to clean and install anchors
- Storm piping/temporary pond installation beginning

## **Budget and Schedule**

Construction Budget: \$46,000,000  
Progress Earned: \$1,438,247.70  
Budget Status: On Budget  
Completion Date: July 1, 2020  
Schedule Status: On Schedule

## **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- July 1, 2020.

## **PREPARED BY:**


- Chris Hubbard, Parrish Construction

## **COPIES TO:**

- Danny Gutlay, APS
- John Rood, Parrish Construction
- Dave Yuhas, Parrish Construction
- Art Cofelice, Parrish Construction
- Andy Webb, Parrish Construction
- Shaun Lindsey, Parrish Construction
- Parrish Construction – Job File

## WEEKLY CONSTRUCTION PROGRESS REPORT

Masonry Restoration installing scaffold in courtyard facing Southeast

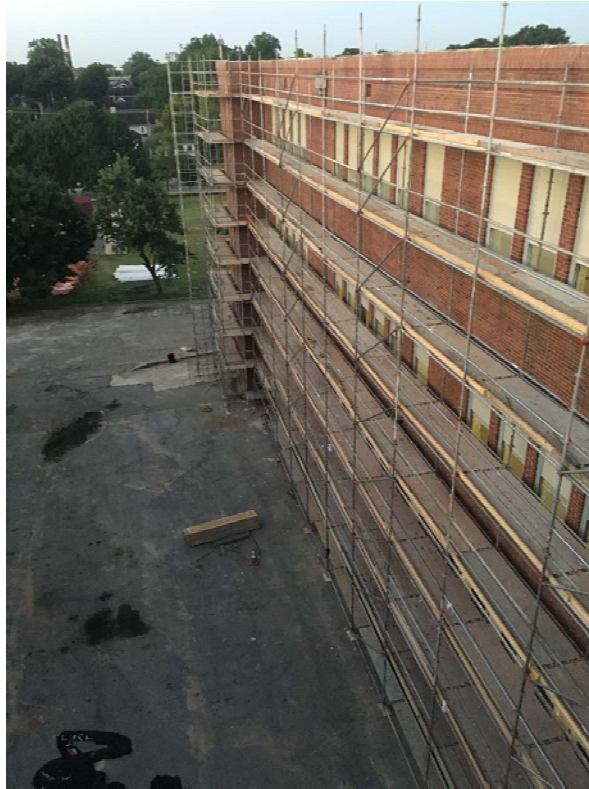

Howard project signs installed on North end of building





## WEEKLY CONSTRUCTION PROGRESS REPORT

Plumbing trenches being cut on first floor



Plumbing trenches being cut on first floor

