

WEEKLY CONSTRUCTION PROGRESS REPORT

Project: Howard Middle School
Week Ending: December 14, 2018

THIS WEEK:

- Curb installation completed on the Northeast parking lot
- Storm piping installation finishing
- Sanitary Sewer Installation finishing
- Brick restoration continuing East side of West Wing
- Concrete footer installation continuing
- Refinishing gym windows continuing
- GeoPiers installation continuing
- Move scaffolding from West wing to East Wing
- Scaffold installed on North side of the building
- Curb installation beginning on the bus lane
- Concrete retaining walls continuing

NEXT WEEK – December 17 thru December 21:

- Installation of brick continuing on the Courtyard side of West Wing
- Refinishing gym windows continuing
- GAB install on the Northeast parking lot (pending weather)
- Geopier installation continuing
- Concrete footer installation continuing
- Concrete retaining wall continuing

Budget and Schedule

Construction Budget: \$46,000,000
Progress Earned: \$3,961,243.57
Budget Status: On Budget
Completion Date: July 1, 2020
Schedule Status: On Schedule

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- July 1, 2020.

PREPARED BY:

- Chris Hubbard, Parrish Construction

COPIES TO:

- Danny Gutlay, APS
- John Rood, Parrish Construction
- Doug Braun Parrish Construction
- Art Cofelice, Parrish Construction
- Shaun Lindsey, Parrish Construction
- Parrish Construction – Job File

WEEKLY CONSTRUCTION PROGRESS REPORT

Project overview facing Southeast



Project overview facing Northwest




WEEKLY CONSTRUCTION PROGRESS REPORT

Scaffolding moved to the South side of East wing



GeoPier installation beginning

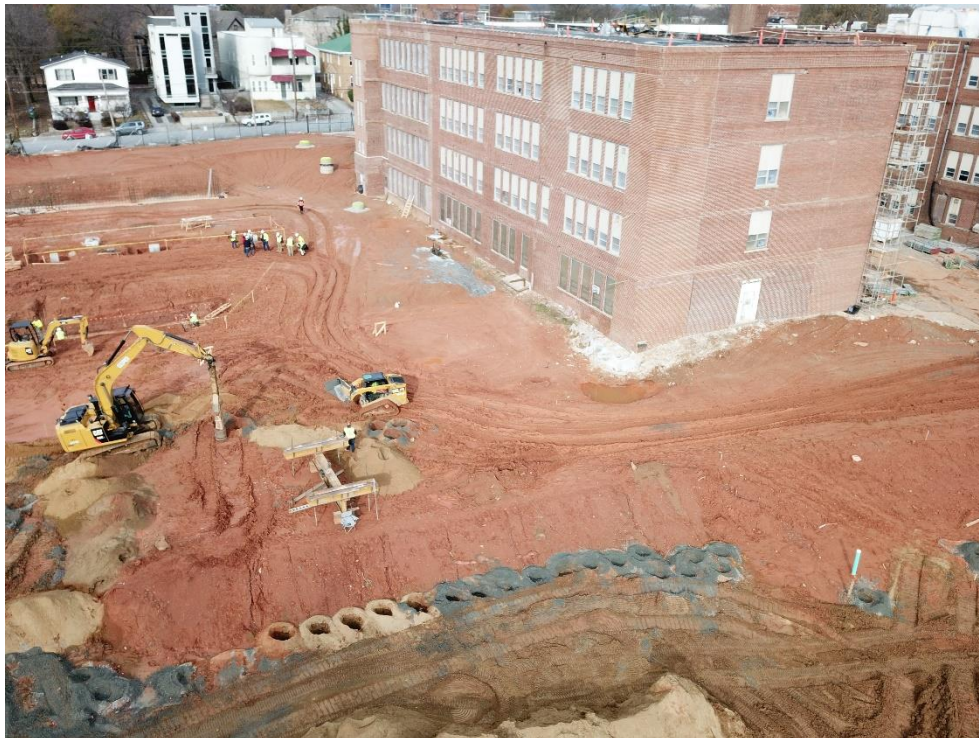

WEEKLY CONSTRUCTION PROGRESS REPORT

Aerial view of Area 1 concrete footers and retaining wall



Access roads being installed

