

WEEKLY CONSTRUCTION PROGRESS REPORT

Project: Howard Middle School
Week Ending: May 31, 2019

THIS WEEK:

- Brick restoration continuing East side of East Wing and North side of building
- MEPS rough in continuing interior West Wing and East Wing
- Area 2 Media columns, formed and placed
- Plaster repair – Existing Building West and East Wing
- West & East Wings Soffit and Partition Framing
- Area 5 Steel Erection, detailing, decking
- Area 1 Cold-formed Metal Framing and sheathing
- Area 1 Spray-on fire proofing and TPO Roofing
- Interior floor repair

NEXT WEEK – June 3 through June 7:

- Brick restoration continuing East side of East Wing and North side of building
- MEPS rough in continuing interior West Wing and East Wing
- Plaster repair – Existing Building West and East Wing
- West & East Wings Soffit and Partition Framing
- Area 5 Steel Erection, detailing, decking
- Area 1 Cold-formed Metal Framing and sheathing
- Area 1 TPO Roofing and detailing
- Area 2 Media SOG
- Existing Interior floor repair

Budget and Schedule

Construction Budget: \$ 46,000,000.00
Progress Earned: \$ 17,110,329.58
Budget Status: On Budget
Completion Date: July 1, 2020
Schedule Status: On Schedule

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- July 1, 2020.

PREPARED BY:

- Shaun Lindsey, Parrish Construction

COPIES TO:

- Danny Gutlay, APS
- John Rood, Parrish Construction
- Art Cofelice, Parrish Construction
- Sandra Horton, APS
- Chris Hubbard, Parrish Construction
- Travis Disbro, Parrish Construction

WEEKLY CONSTRUCTION PROGRESS REPORT



Project Overview looking NW




Area 5 Steel Erection Progress

WEEKLY CONSTRUCTION PROGRESS REPORT



Area 2 Media Center Column & Footings/ UG Plumbing

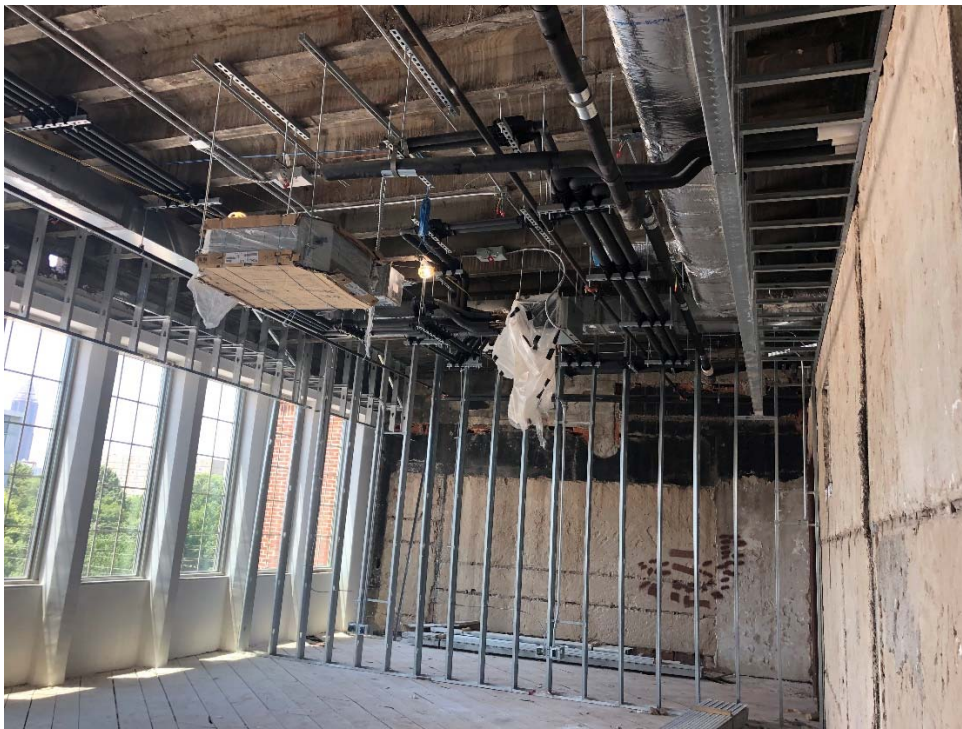

4th floor West Wing – Over Head, walls, and plaster
