

WEEKLY CONSTRUCTION PROGRESS REPORT

Project: Howard Middle School
Week Ending: June 21, 2019

THIS WEEK:

- Brick restoration finished East side of East Wing and continuing on North side of building
- MEPS rough in continuing interior of existing bldg., Area 1, and Area 5
- Plaster repair – Existing Building West and East Wing
- West & East Wings, Area 1 Soffit, Partition Framing, one-side gyp board – 4th floor approved for close-up
- Area 5 Steel detailing and stairs
- Area 1 Cold-formed Metal Framing and sheathing
- Area 5 1st floor elevated slab placement
- Existing Interior floor repair
- Gym Window installation

NEXT WEEK – June 24 through June 28:

- Brick restoration North side of building
- MEPS rough in continuing interior of existing bldg., Area 1, and Area 5
- Plaster repair – Existing Building West and East Wing
- West & East Wings Soffit, Partition Framing, one-side gyp board
- Area 5 Stairs
- Area 1 Cold-formed Metal Framing and sheathing
- Area 5 2nd floor elevated slab placement
- Area 2 Admin Steel Erection
- DOAS Unit 2-1 and 3-1 Setting
- Existing Interior floor repair
- Remaining East windows installed

Budget and Schedule

Construction Budget: \$ 46,000,000.00
Progress Earned: \$ 17,110,329.58
Budget Status: On Budget
Completion Date: July 1, 2020
Schedule Status: On Schedule

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- July 1, 2020.

PREPARED BY:

- Shaun Lindsey, Parrish Construction

COPIES TO:

- Danny Gutlay, APS
- John Rood, Parrish Construction
- Art Cofelice, Parrish Construction
- Sandra Horton, APS
- Chris Hubbard, Parrish Construction
- Travis Disbro, Parrish Construction

WEEKLY CONSTRUCTION PROGRESS REPORT

2nd Floor Elevated Slab Placement




Existing Building Gym Restoration Window Installation



WEEKLY CONSTRUCTION PROGRESS REPORT

Area 5 Metal Stud Walls and Door Frame Installation

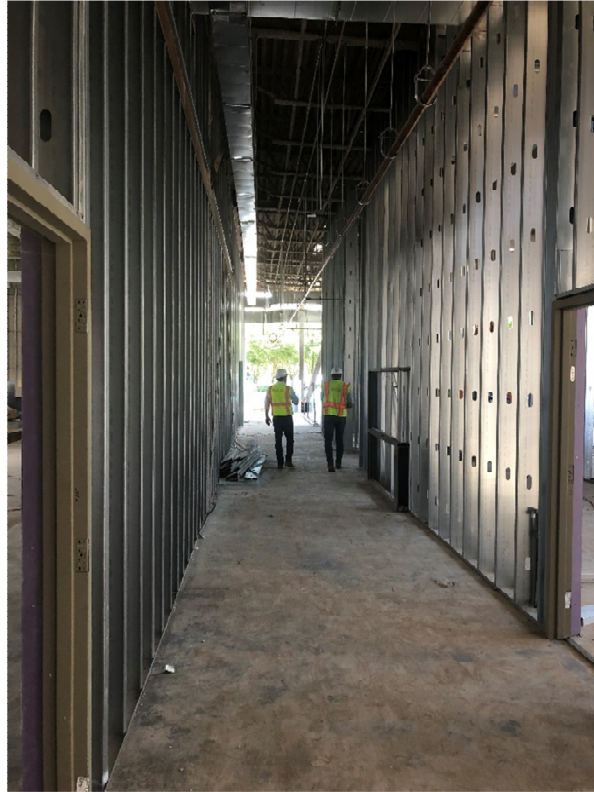

Level 4 Existing building insulation installation beginning

