

WEEKLY CONSTRUCTION PROGRESS REPORT

Project: Howard Middle School
Week Ending: September 20, 2019

THIS WEEK:

- MEPS rough in continuing interior of existing bldg, Area 1, Area 3, & Area 5
- Plaster repair – West wing Stairs
- Area 2 Admin/media slab prep
- Fire proofing continuing in Area 5
- Interior CMU Block walls continuing
- Area 5 Curtain Wall Install
- Gym Roofing Resumes
- Area 4 Steel Detailing
- West & East Wings two side gyp and interior wall gyp lamination
- Area 1 and 5 Metal Framing
- Existing Building Steel Retrofitting
- Area 1 Metal Wall Panel Insulation and z-girts
- Area 5 Sheathing and waterproofing
- Area 5 Brickwork

NEXT WEEK – September 23 – September 27:

- MEPS rough in continuing interior of existing bldg, Area 1, Area 3, & Area 5
- Plaster repair – West wing Stairs
- Area 2 Admin/media slab placement
- Fire proofing continuing in Area 5
- Interior CMU Block walls continuing
- Area 5 Curtain Wall Install
- Gym Roofing Resumes
- Area 4 Steel Detailing
- West & East Wings two side gyp and interior wall gyp lamination
- Area 1 and 5 Metal Framing
- Existing Building Steel Retrofitting
- Area 1 Metal Wall Panel Insulation and z-girts
- Area 5 Sheathing and waterproofing
- Area 5 Brickwork

Budget and Schedule

Construction Budget: \$ 46,000,000.00
Progress Earned: \$ 21,532,703.58
Budget Status: On Budget
Completion Date: July 1, 2020
Schedule Status: On Schedule

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- July 1, 2020.

PREPARED BY:

- Chris Hubbard, Parrish Construction

COPIES TO:

- Danny Gutlay, APS
- John Rood, Parrish Construction
- Art Cofelice, Parrish Construction
- James Jones, Parrish Construction
- Sandra Horton, APS
- Shaun Lindsey, Parrish Construction
- Travis Disbro, Parrish Construction

WEEKLY CONSTRUCTION PROGRESS REPORT

Site view looking Northwest



Area 5 Storefront installation



WEEKLY CONSTRUCTION PROGRESS REPORT

Area 2 (Media center) steel




Area 5 brick work



WEEKLY CONSTRUCTION PROGRESS REPORT

Area 1 Auditorium

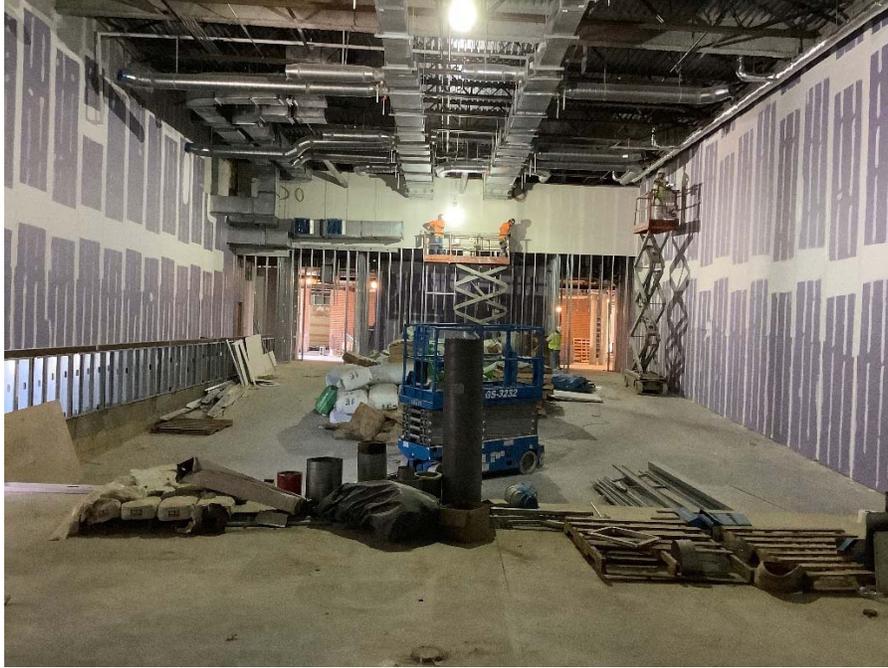

Area 2 Existing 3rd Floor Corridor

