

WEEKLY CONSTRUCTION PROGRESS REPORT

Project: Howard Middle School
Week Ending: October 4, 2019

THIS WEEK:

- MEPS rough in continuing interior of existing bldg, Area 2, Area 3, & Area 5
- Plaster repair – West wing Stairs
- Area 4 Elevated deck Prep
- Fire proofing continuing in Area 5
- Interior CMU Block walls continuing
- Area 5 Curtain Wall Install
- Area 4 Steel Detailing Finish
- Area 5 Sheathing and waterproofing
- West & East Wings interior wall gyp lamination
- Area 1 and 5 Metal Framing
- Area 2 Existing Painting
- Area 1 Metal Wall Panel Insulation and z-girts
- Roof top HVAC equipment set
- Area 5 Brickwork

NEXT WEEK – October 7 – October 11:

- MEPS rough in continuing interior of existing bldg, Area 2, Area 3, & Area 5
- West & East Wings interior wall gyp lamination
- Place Area 4 Elevated concrete deck
- Fire proofing continuing in Area 5
- Interior CMU Block walls continuing
- Area 2 CFM Framing
- Area 5 Curtain Wall Install
- Area 2 Existing Painting
- Area 1 Metal Wall Panel Insulation and z-girts
- Area 5 Sheathing and waterproofing
- Area 5 Brickwork
- Area 1 and 5 Metal Framing

Budget and Schedule

Construction Budget: \$ 46,000,000.00
Progress Earned: \$ 23,538,910.88
Budget Status: On Budget
Completion Date: July 1, 2020
Schedule Status: On Schedule

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- July 1, 2020.

PREPARED BY:

- Chris Hubbard, Parrish Construction

COPIES TO:


- Danny Gutlay, APS
- John Rood, Parrish Construction
- Art Cofelice, Parrish Construction
- Sandra Horton, APS
- Shaun Lindsey, Parrish Construction
- Travis Disbro, Parrish Construction

WEEKLY CONSTRUCTION PROGRESS REPORT

Site view looking Northeast



Area 5 Gang Restroom CMU

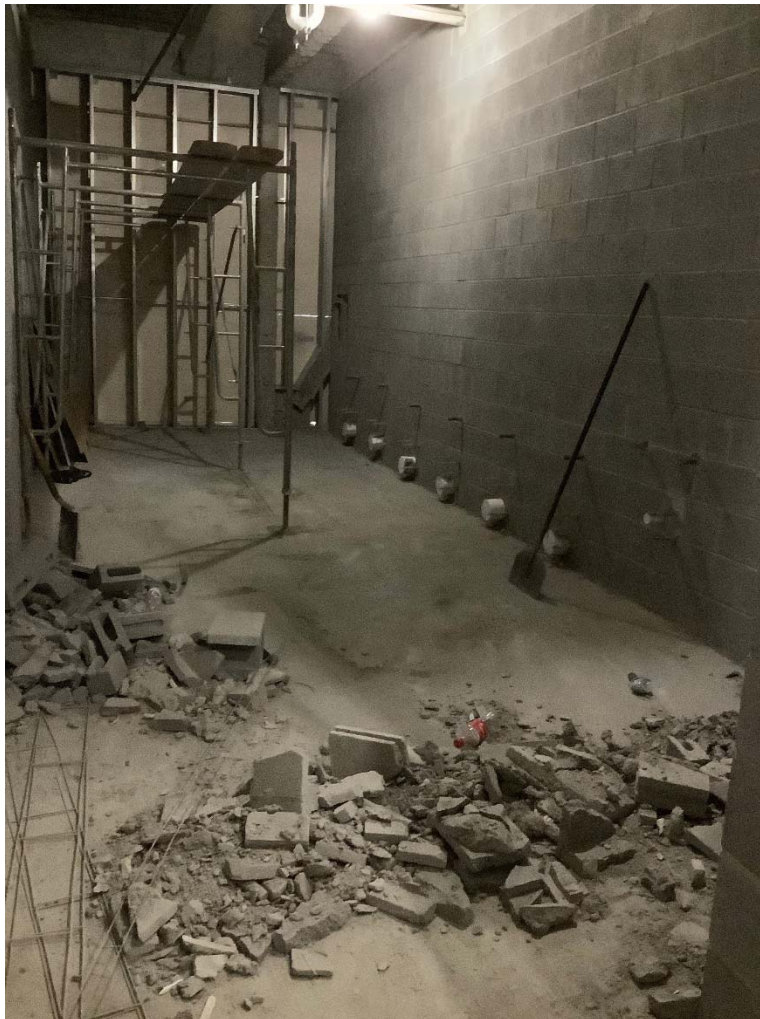


WEEKLY CONSTRUCTION PROGRESS REPORT

Area 4 Elevated Slab Prep'd for Concrete



Area 1 Interior Progress

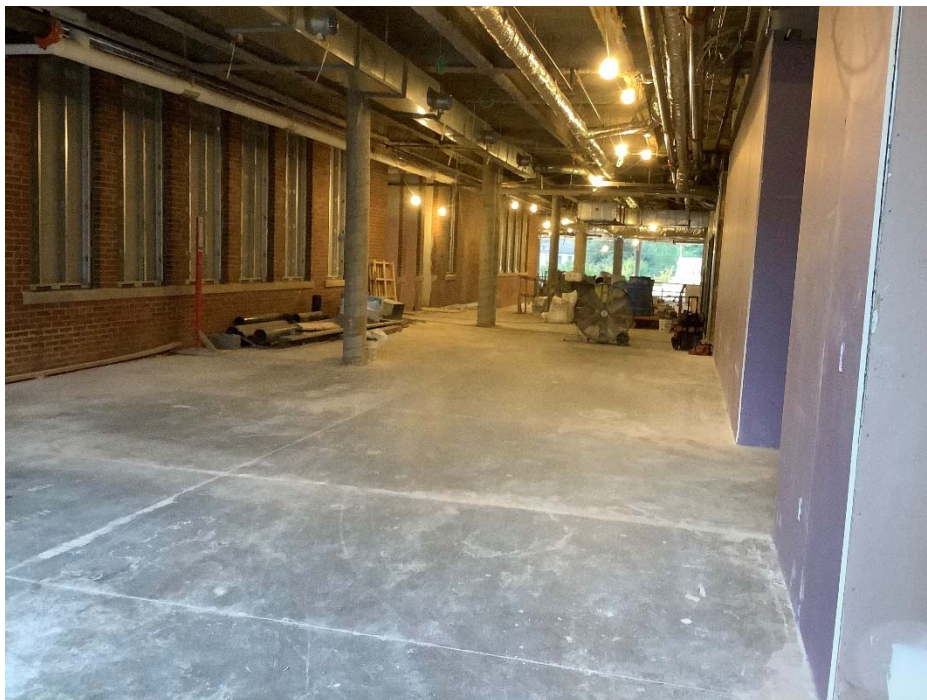

WEEKLY CONSTRUCTION PROGRESS REPORT

Area 1 and 5 HVAC Equipment Setting



Area 5 - View from 4th Floor Classroom

