

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Humphries Elementary School

July 25th, 2019

**Prepared For:** Atlanta Public Schools

**Prepared By:** Tony Washington




Classroom Plumbing Fixture Removal



Classroom Markerboard Removal



Front Gate of Site Fencing

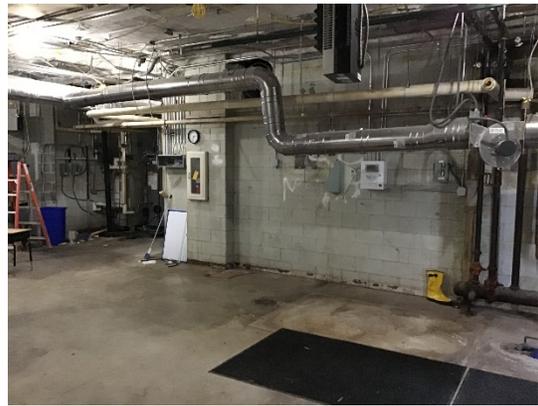

Removal of Mechanical Equipment in Boiler Room



Bathroom Partition Removal



Classroom Ceiling Removal

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Humphries Elementary School

July 25th, 2019



### Last Week's Activities:

- Began mechanical equipment removal
- Began service of existing HVAC equipment
- Began removing markerboards and tack boards
- Began erosion control silt fence installation
- Installed construction entrance
- Completed wood canopy demolition

### This Week's Activities:

- Installed site fencing
- Continued mechanical equipment removal
- Began select interior building demolition
- Completed plumbing fixture removal
- Completed bathroom partition removal
- Completed removing markerboards and tack boards
- Completed millwork removal in building #2030
- Continued electrical demolition

### Next Week's Activities:

- Begin exterior building demolition
- Continue select interior building demolition
- Complete electrical demolition
- Complete mechanical equipment removal
- Begin interior door demolition

### Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

### Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$234,399
