

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

September 12, 2019

Prepared For: Atlanta Public Schools

Prepared By: Tony Washington



CMU Block at Stair 2




Building 2032 Plumbing Piping



Interior Framing at Main Entrance



Building Addition Underground Plumbing

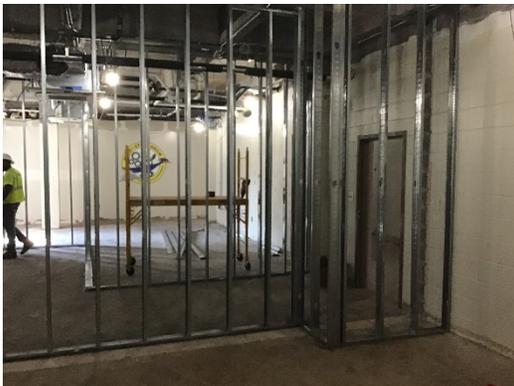

Parent Center Metal Studs



Rerouting Sanitary Line

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

September 12, 2019



Last Week's Activities:

- Completed building foundations
- Completed installing foundations rebar
- Poured remaining building foundations
- Began existing sanitary line removal
- Began sanitary line reroute
- Continued exterior mockup
- Began framing in building #2032
- Completed duct work installation at media center
- Began framing in media center
- Began masonry for stair 2
- Completed interior demolition
- Installed new supply lines in building 2032

This Week's Activities:

- Continued sanitary line reroute
- Began slab on grad prep
- Continue block at stair 2
- Began metal stud infill in renovation buildings
- Continued exterior mockup
- Began refrigerant line removal
- Completed underground plumbing
- Completed plumbing reroutes in building 2032
- Began masonry wall infill

Next Week's Activities:

- Continue sanitary line reroute
- Begin slab on grad
- Continue block at stair 2
- Continue domestic water reroute
- Continue exterior mockup
- Continue refrigerant line removal

Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

September 12, 2019



Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,115,37
