

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

September 26, 2019

Prepared For: Atlanta Public Schools


Prepared By: Tony Washington



CMU Stairs at New Building Addition



Asphalt Demolition at Rear Parking Lot

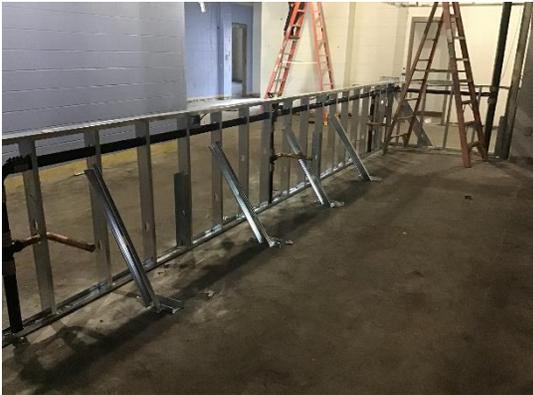

Building 2040 In Wall Rough In



Building 2033 Aluminum Line Removal



Building 2040 MEP Rough In



Complete Sanitary Sewer Reroute

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

September 26, 2019



Last Week's Activities:

- Continued sanitary line reroute
- Poured slab on grade
- Continued CMU block at stair 2
- Continued exterior mockup
- Continued refrigerant line removal
- Continued interior framing
- Continued CMU block infill in building 2033
- Completed underground plumbing in building 2033
- Completed framing in building 2032

This Week's Activities:

- Began framing in boiler room
- Began plumbing in wall rough in
- Began asphalt removal at rear parking lot
- Continued metal framing infill
- Continued exterior mockup
- Continued refrigerant line removal
- Continued CMU block infill
- Completed sanitary line reroute
- Completed CMU block at stair 2

Next Week's Activities:

- Begin new ductwork install in building 2032
- Begin level 1 steel erection at new addition
- Begin underground Georgia Power electrical reroute
- Begin domestic water reroute
- Complete asphalt removal in rear parking lot
- Begin StormTech excavation

Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,115,370
