

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

September 27, 2019



Prepared For: Atlanta Public Schools

Prepared By: Tony Washington



Classroom Partition Demolition



Partition Demolition at Hallway




Classroom VCT Flooring Demolition



Cafeteria Ceiling Grid Demolition



Media Center Partition Demolition

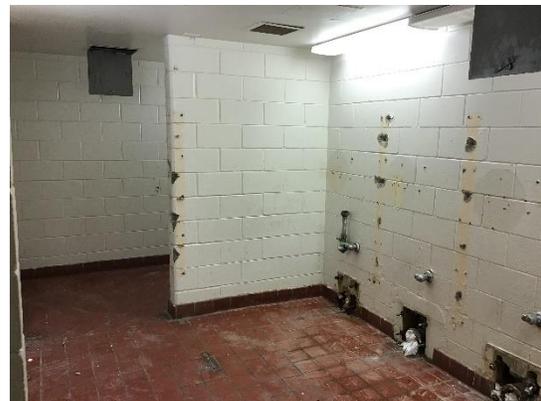

Bathroom Partition Demolition

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

September 27, 2019



Last Week's Activities:

- Installed jobsite perimeter fencing
- Installed APS SPLOST signage
- Began selective MEP demolition
- Began selective interior demolition

This Week's Activities:

- Installed jobsite signage
- Continued selective MEP demolition
- Continued selective interior demolition
- Began service inventory of existing HVAC equipment

Next Week's Activities:

- Continue selective MEP demolition
- Continue selective interior demolition
- Continue service inventory of existing HVAC equipment
- Begin cleaning out existing grease traps

Schedule:

- Status: On Schedule

Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$373,962
