

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

October 03, 2019

Prepared For: Atlanta Public Schools

Prepared By: Tony Washington



Building Addition Steel Erection




Building Addition Steel Erection



Asphalt Demolition at Rear Parking Lot



New Electrical Room Panels

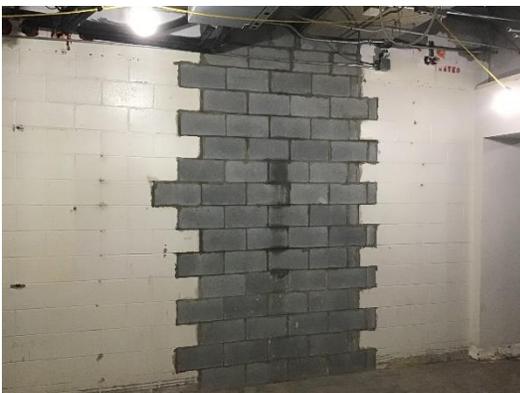

Building 2033 CMU Block Infill



Exterior Stair Demolition

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

October 03, 2019



Last Week's Activities:

- Began framing in boiler room
- Began plumbing in wall rough in
- Began asphalt removal at rear parking lot
- Continued exterior mockup
- Continued metal framing infill
- Continued refrigerant line removal
- Continued CMU block infill
- Completed sanitary line reroute

This Week's Activities:

- Continued CMU block Infill
- Continued CMU block at Stair 2
- Continued refrigerant line removal
- Completed overhead MEP in building 2033
- Continued asphalt removal in rear parking lot
- Completed new ductwork install in building 2032
- Began level 1 steel erection at new building addition
- Began level 2 beams at new building addition
- Began domestic water reroute
- Continued framing in boiler room

Next Week's Activities:

- Begin new ductwork install in building 2040
- Begin underground Georgia Power electrical reroute
- Complete level 1 steel erection at new building addition
- Complete level 2 beams at new building addition
- Begin level 2 decking at new building addition
- Continue domestic water reroute

Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,957,883
