

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

October 24, 2019

Prepared For: Atlanta Public Schools

Prepared By: Tony Washington



Building Addition Front View




Building 2040 New Ductwork



Front View of Exterior Mockup



Building 2031 Shingled Roof

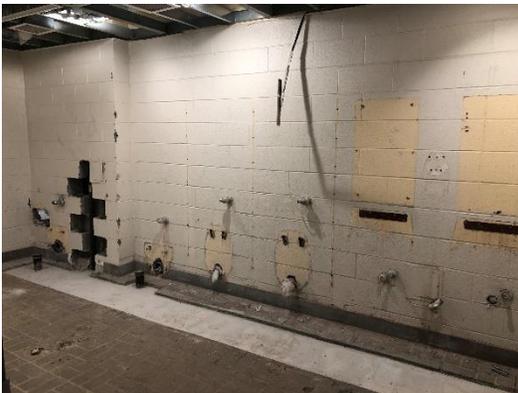

Building 2032 Concrete Pour Back For Plumbing



Building 2032 Sprinkler Piping

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

October 24, 2019



Last Week's Activities:

- Began sprinkler system installation at building 2032
- Completed level 2 decking at new building addition
- Continued domestic water reroute
- Completed new ductwork install in building 2040

This Week's Activities:

- Began canopy drainage system
- Began building 2030 roof decking
- Began sprinkler system install at building 2033
- Completed building 2030 steel detailing
- Completed sprinkler system installation at building 2032
- Completed shingle roof replacement on building 2031
- Continued domestic water reroute
- Installed gymnasium lighting

Next Week's Activities:

- Complete domestic water reroute
- Complete canopy drainage system
- Continue building 2033 sprinkler installation
- Pour building 2030 elevated slab
- Begin Stormtech at parking lot

Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,957,883
