

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

October 25, 2019



**Prepared For:** Atlanta Public Schools


**Prepared By:** Tony Washington



First Floor Classroom Framing



Second Floor Hallway Framing

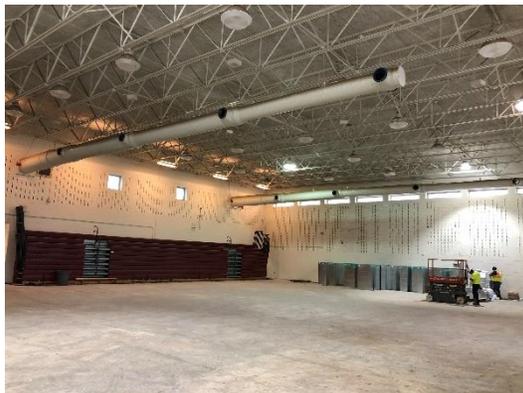

Gymnasium Ductwork Branch Line Demo



Ductwork installation at Second Floor



Saw Cutting at New Culinary Arts Lab



Saw Cutting at New Dental Lab

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

October 25, 2019



### Last Week's Activities:

- Began second floor interior framing
- Continued selective MEP demolition
- Continued selective interior demolition

### This Week's Activities:

- Began saw cutting for underground plumbing
- Began second floor ductwork installation
- Began first floor interior framing
- Continued second floor interior framing
- Continued selective interior demolition
- Continued selective MEP demolition

### Next Week's Activities:

- Begin structural supports for concrete deck openings
- Continue saw cutting for underground plumbing
- Continue second floor ductwork installation
- Continue selective interior demolition
- Complete selective MEP demolition

### Schedule:

- Status: On Schedule

### Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$465,806
