


WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

November 21, 2019

Prepared For: Atlanta Public Schools

Prepared By: Tony Washington

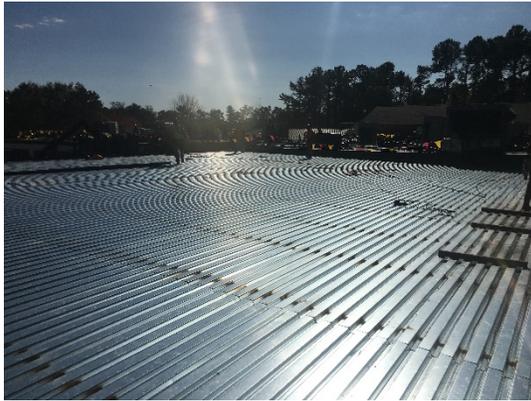

Roof Decking at New Addition



New Roof Installation at Existing Buildings



Exterior Framing at New Addition



MEP Rough in at New Addition



Stormtech Excavation



Interior Framing at New Addition

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

November 21, 2019



Last Week's Activities:

- Completed bent plate installation at building 2030
- Completed domestic water reroute
- Continued roof installation at building 2033 & 2040
- Continued drywall installation at building 2031
- Began roof decking on new addition
- Began exterior framing at new addition
- Began interior framing at new addition
- Completed courtyard storm line installation
- Began final grade at East elevation
- Began duct work installation at new addition
- Continued level 2 sprinkler installation

This Week's Activities:

- Continued roof installation at building 2033 & 2040
- Completed drywall installation at building 2031
- Completed roof decking on new addition
- Completed exterior framing at new addition
- Continued interior framing at new addition
- Continued final grade at East elevation
- Continued duct work installation at new addition
- Continued level 2 sprinkler installation
- Began MEP rough in at the new addition
- Began sheathing exterior of new addition
- Began stormtech excavation and installation

Next Week's Activities:

- complete Stormtech at parking lot
- Complete interior framing at new addition
- Began hanging HI drywall at new addition
- Complete roof installation at building 2033 & 2040
- Begin roof installation at new addition
- Continue MEP installation at new addition
- Begin canopy foundations
- Set new generator at courtyard
- Pour metal stair stringers
- Complete level 2 sprinkler system

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

November 21, 2019



Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,957,883
