

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

November 22, 2019



Prepared For: Atlanta Public Schools


Prepared By: Tony Washington



Ductwork Installation at First Floor



Ductwork Installation at Auto/Aviation Labs

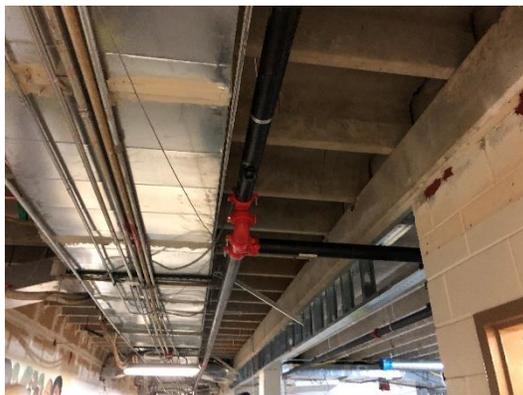

Sprinkler Piping Installation at Second Floor



Backfill at Culinary Arts Lab



Drywall on Site at Auto/Aviation Labs



Sawcutting at Auto/Aviation Labs

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

November 22, 2019



Last Week's Activities:

- Continued second floor ductwork installation
- Continued underground plumbing
- Continued interior framing
- Continued CMU block infill
- Continued in-wall electrical rough in
- Continued ductwork installation at Automotive & Aviation Labs

This Week's Activities:

- Continued second floor ductwork installation
- Continued first floor ductwork installation
- Continued in-wall electrical rough in
- Continued interior framing
- Completed ductwork installation at Automotive & Aviation Labs
- Completed backfill at Culinary Arts Lab
- Began demo for openings at Automotive & Aviation Labs
- Began plumbing rough in at Automotive & Aviation Labs
- Began sprinkler piping installation

Next Week's Activities:

- Continue CMU block infill
- Continue first floor ductwork installation
- Continue second floor ductwork installation
- Continue in-wall electrical rough in
- Continue interior framing
- Continue demo for openings at Automotive & Aviation Labs
- Continue plumbing rough in at Automotive & Aviation Labs
- Continue sprinkler piping installation
- Continue underground electrical rough in at Culinary Arts Lab
- Continue slab preparation at Culinary Arts Lab

Schedule:

- Status: On Schedule

Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,043,624
