

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

December 12, 2019



**Prepared For:** Atlanta Public Schools


**Prepared By:** Tony Washington




Metal Framing at Main Entrance



Electrical Rough-In at Culinary Arts Lab

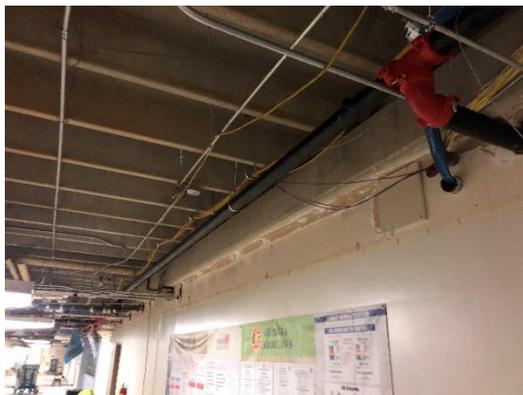


Sprinkler Piping at Second Floor

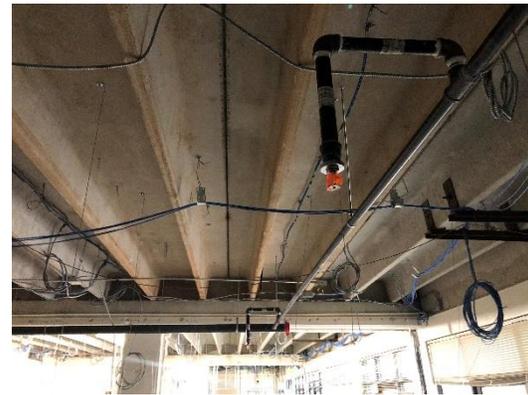

Sprinkler Head Installation at Second Floor



Sanitary Sewer Structures On Site

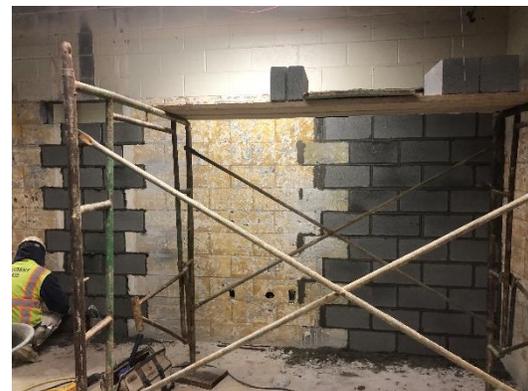

Masonry Block Infill at Auto/Aviation Labs

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

December 12, 2019



### Last Week's Activities:

- Poured slab at Culinary Arts Lab
- Continued CMU block infill
- Continued first floor ductwork installation
- Continued second floor ductwork installation
- Continued in-wall electrical rough in
- Continued interior framing
- Continued plumbing rough in at Automotive & Aviation Labs
- Continued slab prep at Automotive & Aviation Labs
- Continued sprinkler piping installation
- Poured slab at Automotive & Aviation labs

### This Week's Activities:

- Continued CMU block infill
- Continued first floor ductwork installation
- Completed second floor ductwork installation
- Continued in-wall electrical rough in
- Continued in-wall plumbing rough in
- Continued interior framing
- Completed angle supports installation at first floor.
- Continued sprinkler piping installation

### Next Week's Activities:

- Continue CMU block infill
- Complete first floor ductwork installation
- Continue in-wall electrical rough in
- Continue in-wall plumbing rough in
- Continue interior framing
- Begin shoring for openings at Automotive & Aviation Labs
- Continue sprinkler piping installation
- Begin demolition of asphalt drive at Auto & Aviation Labs

### Schedule:

- Status: On Schedule

### Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,714,024
