



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 10/09/20

THIS WEEK

- Tree removal continuing
- Demolition of flooring, ceilings, and walls continuing in Area 1 and 2 continuing
- Demolition in Area 4 beginning
- Electrical and Plumbing rough-in beginning in Area 1 and 2.
- HVAC relocation beginning
- New media center grading beginning

NEXT WEEK: 10.12.20 – 10.16.20

- Tree removal continuing
- Demolition of flooring, ceilings, and walls continuing in Area 4
- Electrical and Plumbing rough-in continuing in Area 1 and 2.
- HVAC relocation continuing
- Metal stud walls installation beginning in Area 1
- Media center grading continuing

BUDGET

Construction Budget

\$10,900,000.00

Budget Status

\$421,596.53

Completed By:
Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo Updates


Media Center Grading



Area 1 Plumbing Rough-in



1st Floor- Area 2 Floor Demo

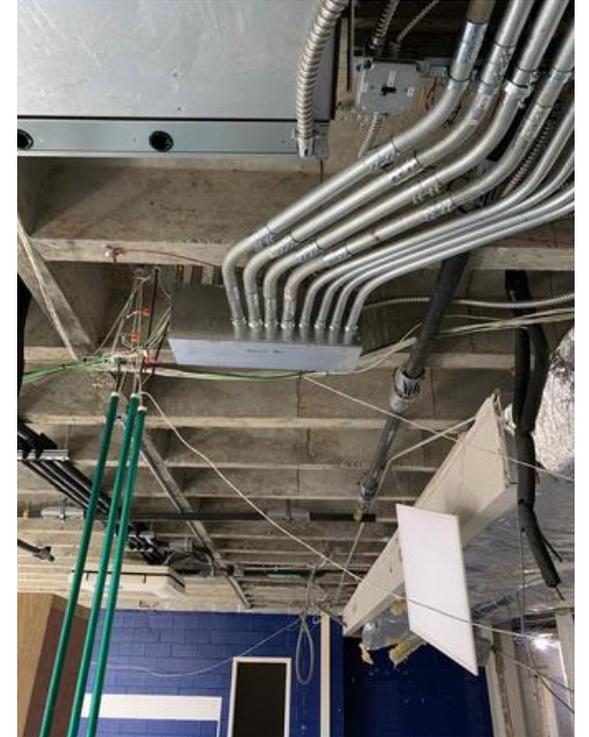

Electrical Relocation

