



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 10/23/20

THIS WEEK

- Demolition of flooring, ceilings, and walls continuing in Area 3 and 4 continuing
- Electrical and Plumbing rough-in continuing in Area 1 and 2.
- Plumbing rough-in beginning in Area 3
- HVAC relocation continuing
- New media center grading finishing
- Media Center underground plumbing finishing
- New gym addition site demolition complete
- Underground storm pond installation beginning

NEXT WEEK: 10.26.20 – 10.30.20

- Electrical and Plumbing rough-in continuing in Area 1 and 2.
- Electrical and plumbing rough-in continuing in Area 3.
- HVAC relocation continuing
- Metal stud walls installation beginning in Area 1
- Media center footing installation beginning
- New gym addition grading continuing
- Underground storm pond installation continuing

BUDGET

Construction Budget

\$10,900,000.00

Budget Status

\$421,596.53

Completed By:
Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo Updates


Media Center
subgrade prep



Underground
pond install



Gym addition
grading

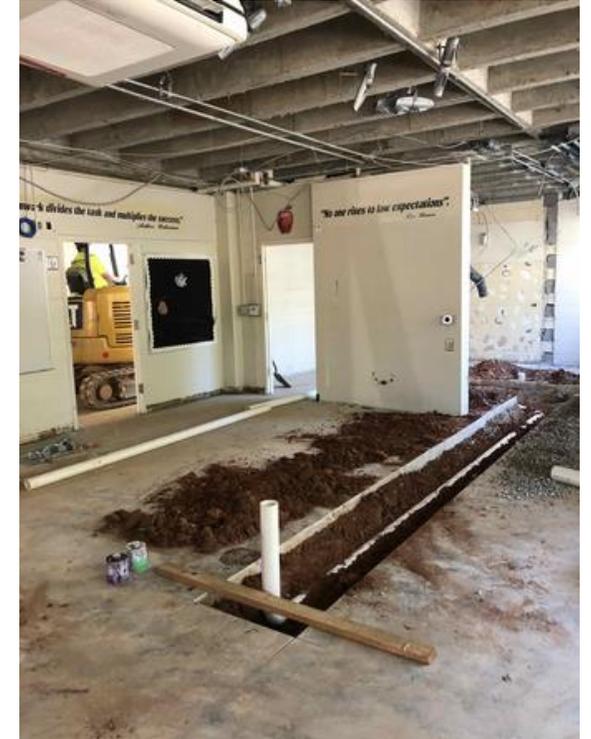

Underground
plumbing Area 3

