



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 11/06/20

### THIS WEEK

- Demolition of flooring, ceilings, and walls continuing in Area 3 and 4 finishing
- Electrical and Plumbing rough-in continuing in Area 2&3.
- HVAC relocation continuing
- New gym addition grading continuing
- Underground storm pond and storm structures installation continuing
- Media Center and Vestibule slab on grade complete
- Fire Suppression rough-in continuing in Area 1
- Metal stud install continuing in Area 1 and beginning in Area 2

### NEXT WEEK: 11.09.20 – 11.13.20

- Electrical and plumbing rough-in continuing in Area 2 and Area 3.
- HVAC relocation continuing
- Metal stud walls installation continuing in Area 1 and Area 2
- New gym addition grading continuing
- New gym footings beginning
- Underground storm pond installation finishing
- Fire suppression continuing in Area 1.

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status

\$638,977.79

Completed By:  
Chris Hubbard

**PARRISH**  
CONSTRUCTION GROUP

# Photo Updates




Media Center slab  
on grade



Underground  
Storm Pond



Vestibule slab on  
grade

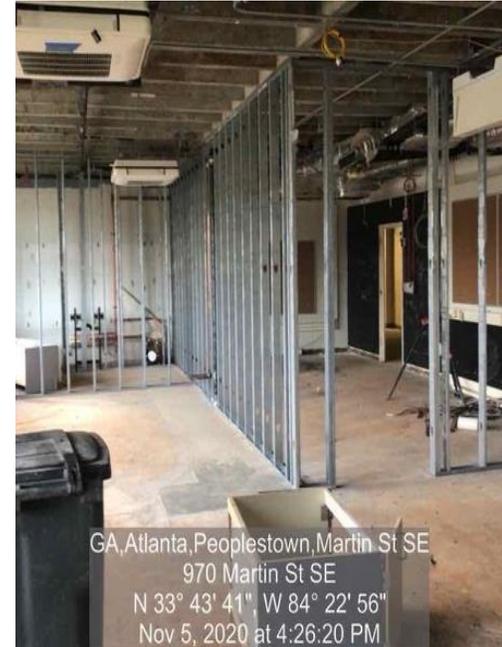

Metal framing  
Area 2

