



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 11/13/20

THIS WEEK

- Electrical and Plumbing rough-in continuing in Area 3&4.
- HVAC relocation continuing
- Underground storm pond and storm structures installation completing
- Fire Suppression rough-in continuing in Area 1
- Metal stud install continuing in Area 1 and beginning in Area 2
- New gym addition grading continuing

NEXT WEEK: 11.16.20 – 11.20.20

- Electrical and plumbing rough-in continuing in Area 2, 3 & 4.
- HVAC relocation continuing
- Metal stud walls installation continuing in Area 2 & 3
- New gym footings beginning
- Fire suppression continuing in Area 1 & 2.
- HVAC completing in Area 1

BUDGET

Construction Budget

\$10,900,000.00

Budget Status

\$638,977.79

Completed By:
Chris Hubbard

PARRISH
CONSTRUCTION GROUP


Photo Updates

Underground Pond Install



Storm Structure Installation

Plumbing Area 3

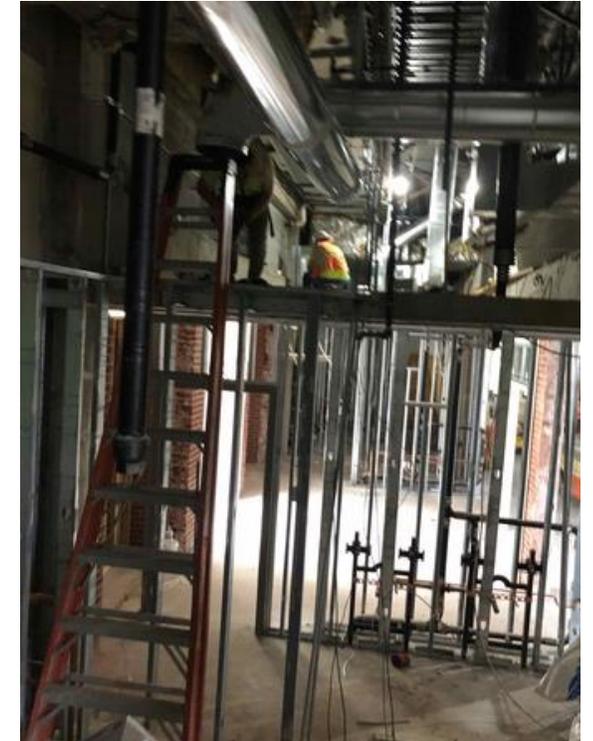

Metal framing & Ductwork Area 1

