



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 12/04/20

### THIS WEEK

- Electrical and Plumbing rough-in continuing in Area 2, 3 & 4.
- HVAC relocation continuing
- Gym foundation block beginning
- Fire Suppression rough-in continuing in Area 1, 2 & 3
- Metal stud install continuing in Area 2, 3, and 4.
- Masonry patching continuing
- Roofing continuing
- Fire alarm upgrades continuing
- Drywall installation continuing
- Beginning gym building pad
- Door frame installation
- Auditorium painting beginning

### NEXT WEEK: 12.07.20 – 12.11.20

- Electrical and plumbing rough-in continuing in Area 2, 3 & 4.
- HVAC relocation continuing
- Metal stud walls installation continuing in Area 2, 3 & 4
- Fire suppression continuing in Area 1, 2 and 3
- Roofing continuing on auditorium/cafeteria building
- Fire alarm upgrades continuing
- Gym cast in place concrete walls installation finishing
- Door frame installation continuing
- Media Center and Vestibule structural steel install beginning

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status

\$2,204,953.25

Completed By:  
Chris Hubbard

**PARRISH**  
CONSTRUCTION GROUP

# Photo Updates


Electrical Panel



Drywall beginning



Auditorium  
Painting

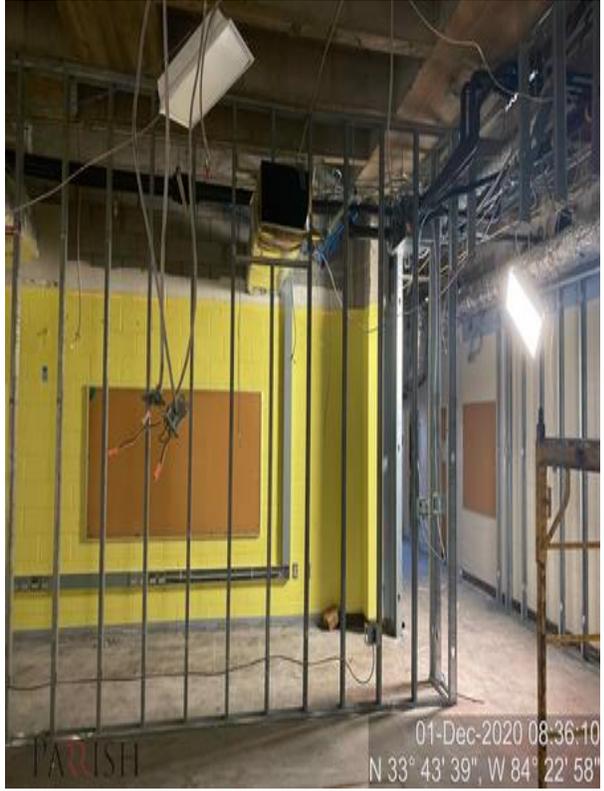

Metal Stud Install

