



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 12.18.2020

### THIS WEEK

- Electrical and plumbing rough-in continuing in Area 2, 3 & 4.
- HVAC relocation continuing
- Metal stud walls installation continuing in Area 2, 3 & 4
- Drywall installation continuing in Area 1 and 2
- Fire suppression continuing in Area 1, 2 and 3
- Roofing beginning in Area 2
- Gym building pad grading continuing
- Door frame installation continuing
- Media Center and Vestibule structural steel install beginning
- Vestibule metal deck install

### NEXT WEEK: 12.21.20 - 12.25.20

- Electrical and plumbing rough-in continuing in Area 2, 3 & 4.
- HVAC relocation continuing
- Metal stud walls installation finishing in Area 2, 3 & 4
- Drywall installation continuing
- Fire suppression continuing in Area 1, 2 and 3
- Roofing continuing in Area 2
- Underslab electrical and plumbing beginning
- Door frame installation continuing
- Media Center and Vestibule structural steel install continuing
- Christmas break will be 12.24 through 12.27

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status

\$2,204,953.25

Completed By:  
Chris Hubbard


**PARRISH**  
CONSTRUCTION GROUP

# Photo Updates

Duct work in Area 3



Steel deck installed on Vestibule

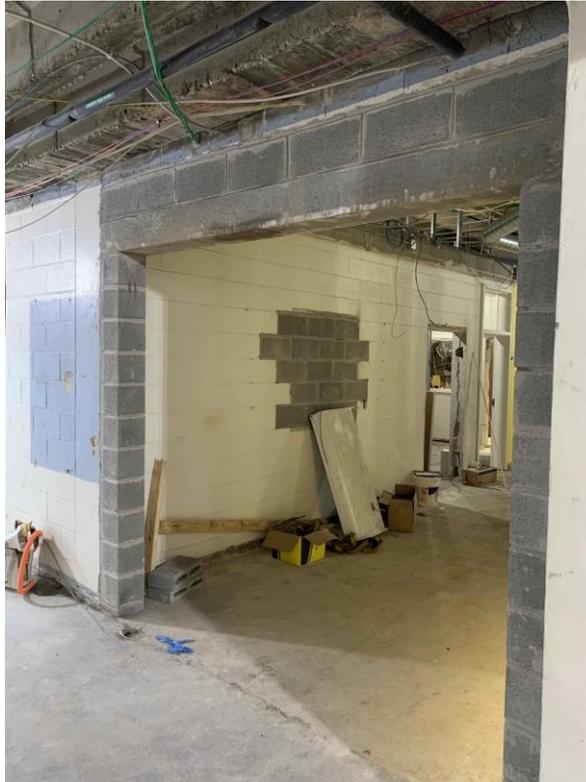

New door opening in Area 3



New handicap accessible opening

