



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 12.25.2020

THIS WEEK

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Fire suppression continuing in Area 3 and beginning in Area 4
- Roofing continuing in Area 2
- Wall primer installation beginning
- Electrical and plumbing underground rough-in
- Erosion Control measures
- Door frame installation continuing
- Media center structural steel install continuing
- Slab preparation beginning
- Christmas break will be 12.24 through 12.27

NEXT WEEK: 12.28.20 – 01.01.21

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing beginning
- Ceiling grid installation in Area 1
- Wall primer installation continuing
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2
- Door frame installation continuing
- Media center structural steel install continuing
- Slab preparation continuing
- New Year's break will be 11.31 through 01.03

BUDGET

Construction Budget

\$10,900,000.00

Budget Status

\$2,204,953.25

Completed By:
Chris Hubbard

PARRISH
CONSTRUCTION GROUP



Photo Updates

Foundation Wall waterproofing



Underground Plumbing rough-in

Erosion Control

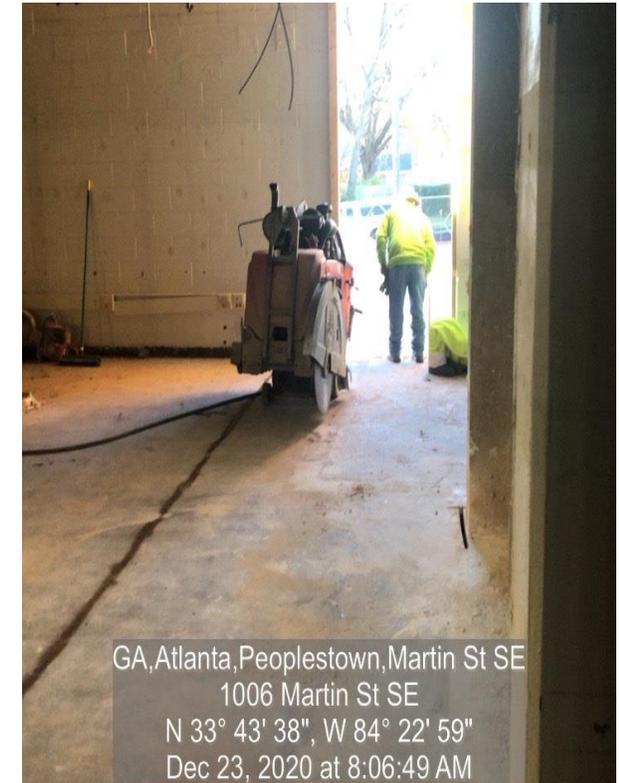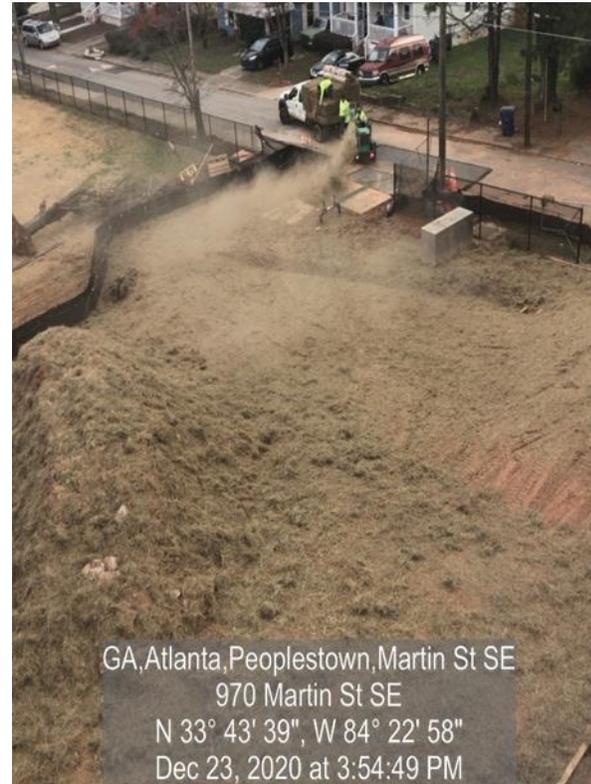

Concrete Cutting at handicap opening

