



Weekly Construction Progress Report

Howard Middle School
Week Ending: 3/27/20

PARRISH
CONSTRUCTION GROUP

Weekly Updates

THIS WEEK

- MEP rough in continuing Area 3
- MEP Fixtures and trim out in Area 1, 2, 4 and 5
- Area 3/4 CFM Framing and sheathing
- Area 4/Bridge Curtain Wall
- Exterior Curb, Gutter, GAB, Sidewalks
- Area 5 Metal Wall Panel and ACM
- Area 3 and 5 hang and finish gyp
- MEP Startups
- Area 3 Wall Tile and Epoxy flooring
- Area 1,2,5 Painting
- Mark Products Casework Install
- Fire Alarm and Low Voltage Startups
- Landscaping Install

NEXT WEEK: 3.30.20 – 4.02.20

- MEP rough in continuing Area 3
- MEP Fixtures and trim out in Area 1, 2, 4 and 5
- Area 3/4 CFM sheathing and Vapor Barrier
- Area 4/Bridge Curtain Wall
- Exterior Curb, Gutter, GAB, Sidewalks
- Area 5 Metal Wall Panel and ACM
- Area 3 and 5 hang and finish gyp
- MEP Startups
- Area 3 Wall Tile and Epoxy flooring
- Area 1,2,5 Painting
- Mark Products Casework Install
- Fire Alarm and Low Voltage Startups
- Install of Steel Ladders and Handrails
- Vertical Expansion Control and Control Joint Caulking
- Gym TPO roof



Budget & Schedule

BUDGET

Construction Budget

- \$46,000,000.00

Budget Status

- \$40,568,072.41

SCHEDULE

Completion Date

- July 1, 2020

Schedule Status

- On Schedule



ADDITIONAL INFO

- Scheduled Substantial Completion Date
 - July 1, 2020
- Completed By
 - Shaun Lindsey
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - John Rood, PCG
 - Art Cofelice, PCG
 - Chris Hubbard, PCG
 - Shaun Lindsey, PCG



Photo Updates

Site View facing NW



Site View Facing NW



Photo Updates

NW corner of Site – Auditorium & Music Rooms



NW Corner of Site street Level



Photo Updates

SW corner of Classroom Building



Typical Classroom in Classroom Bldg



Photo Updates

Area 2 – North Corridor 3rd Fl



Cafeteria Ceiling – final finishing



Photo Updates

Shade Garden




Shade Garden



Photo Updates

Media Center – Courtyard Entrance

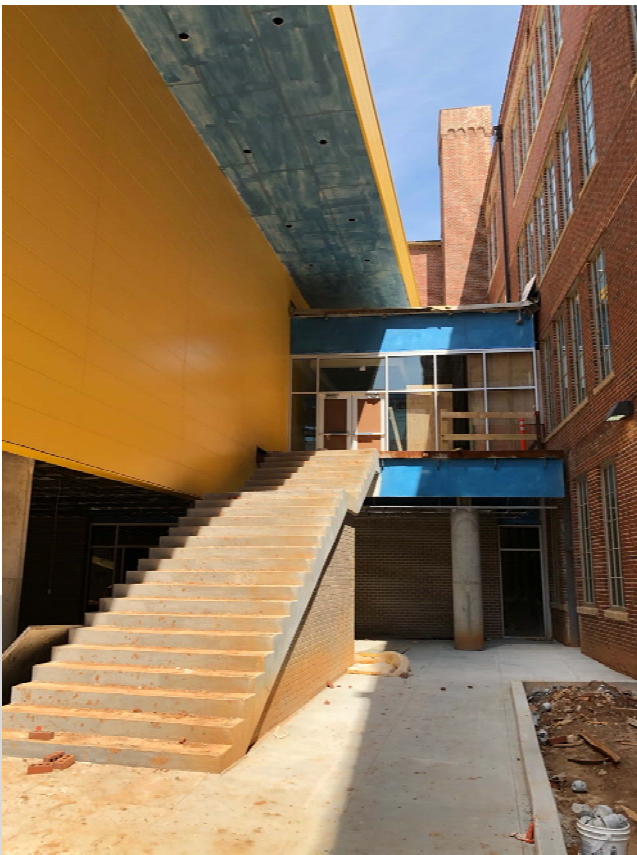


Media Center Entrance Lobby



Photo Updates

Existing Bldg – N. Corridor Lvl 1

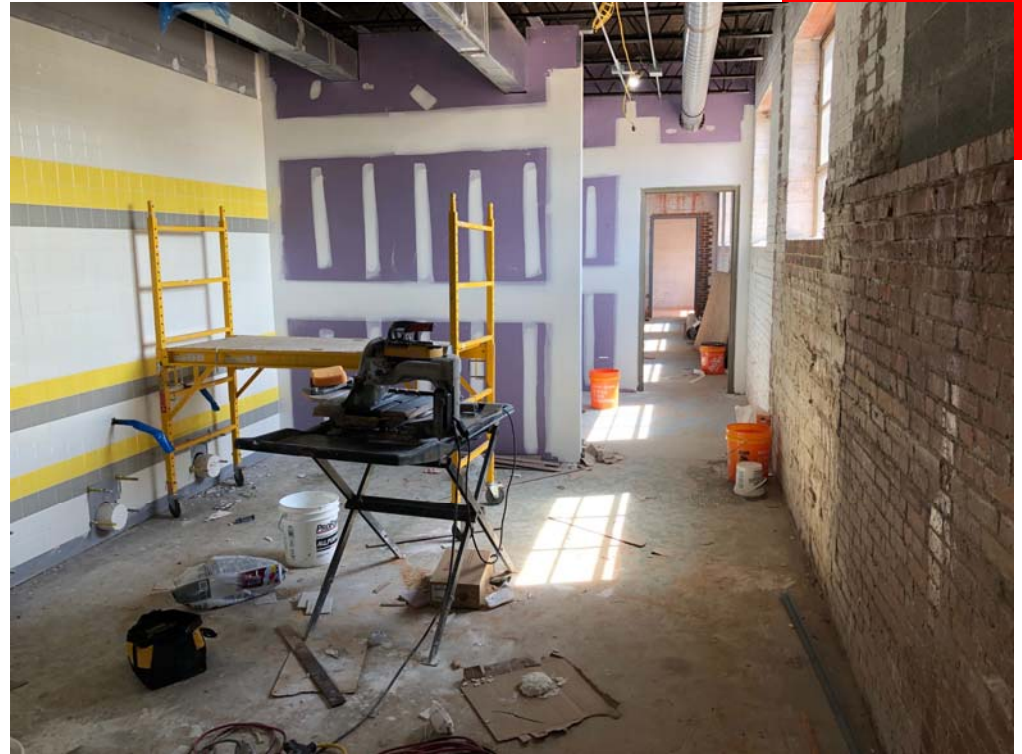

Gym Locker Rooms

