

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

March 13, 2020



Prepared For: Atlanta Public Schools


Prepared By: Tony Washington



Structural Steel Installed at Auto Lab Openings



Structural Steel Installed at Aviation Openings

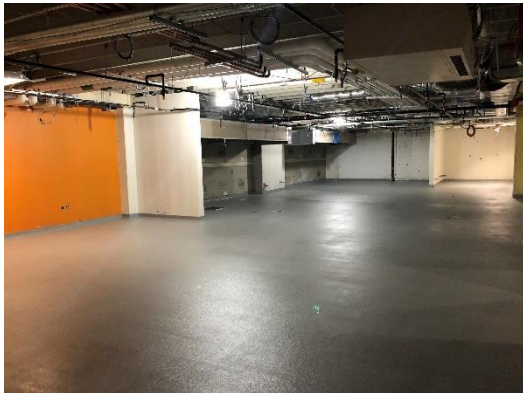


Epoxy Flooring at Culinary Arts Lab



Epoxy Flooring at Cafeteria Kitchen



Second Floor Classroom New Light Fixtures

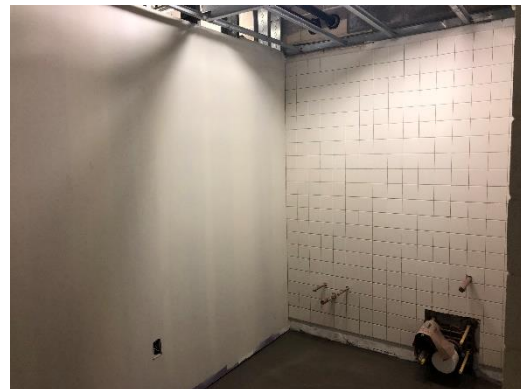

First Floor Restroom Wall Tile & Priming

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

March 13, 2020



Last Week's Activities:

- Continued sprinkler piping at the first floor
- Completed wall tile installation at restrooms
- Poured footings for steel columns at Auto/Aviation Labs
- Continued electrical panel wire pull
- Began prep for epoxy flooring at Cafeteria Kitchen & Culinary Arts Lab
- Continued installation of vertical fan coil units
- Continued second floor ceiling grid installation
- Continued installation of vertical fan coil units
- Completed drywall installation at Aviation Lab
- Completed installation of rooftop condenser stands

This Week's Activities:

- Continued sprinkler piping at the first floor
- Completed wall tile installation at restrooms
- Installed epoxy flooring at Cafeteria Kitchen & Culinary Arts Lab
- Continue electrical panel wire pull
- Began installation of new light fixtures
- Continued priming and first coat of paint
- Continued installation of vertical fan coil units
- Continued ceiling grid installation
- Began new water line installation
- Continued controls wiring at first floor
- Completed installation of structural steel at Auto/Aviation Lab openings

Next Week's Activities:

- Continue sprinkler piping at the first floor
- Install stained concrete flooring at Cafeteria
- Continue new water line installation
- Complete electrical panel wire pull
- Continue installation of new light fixtures
- Complete priming and first coat of paint
- Continue installation of vertical fan coil units
- Continue ceiling grid installation
- Continue controls wiring at first floor
- Pour back footings for steel columns at Auto/Aviation Lab
- Begin second coat of paint at second floor
- Continue epoxy flooring at restrooms

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

March 13, 2020



Schedule:

- Status: On Schedule

Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$5,318,229
