

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

April 03, 2020



Prepared For: Atlanta Public Schools

Prepared By: Tony Washington



Automotive Lab Sectional Doors Installed



Exterior Paint at Front of Main Building




Ceiling Tile Installed at Reception Area 202



Ceiling Tile Installed at I.T. Lab 222



Ceiling Grid Installed at Corridor 157

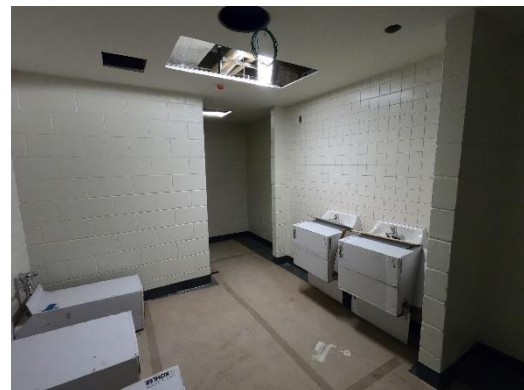

Restroom 249 Plumbing Fixtures Installed

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

April 03, 2020



Last Week's Activities:

- Continued sprinkler head drops at first floor
- Completed new water line installation
- Continued installation of new light fixtures
- Continued piping installation for vertical fan coil units
- Continued ceiling grid installation
- Continued plumbing fixture installation at restrooms
- Began ceiling grid installation at first floor

This Week's Activities:

- Continued sprinkler piping at the first floor
- Completed installation of sectional doors at Auto/Aviation Lab
- Completed sanitary sewer tie-in to existing
- Continued electrical panel wire pull
- Continued installation of new light fixtures
- GAB installed at Auto/Aviation Lab Drive
- Completed final coat of paint at second floor
- Continued ceiling grid installation at first floor
- Completed installation of FRP panels at Culinary Arts Lab
- Began installation of concrete curbs and flatwork
- Continued installation of devices for vertical fan coil units
- Began installation of HVAC diffusers
- Completed piping installation for vertical fan coil units
- Continued exterior paint at main building
- Continued installation of plumbing fixtures at restrooms
- Began painting of exposed ceilings at second floor

Next Week's Activities:

- Continue first floor prep. for sealed concrete
- Complete installation of HVAC diffusers
- Continue installation of new light fixtures
- Continue exterior paint at main building
- Continue installation of vertical fan coil units
- Continue ceiling grid installation
- Continue installation of plumbing fixtures at restrooms
- Continue paint of exposed ceilings at second floor

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

April 03, 2020



Schedule:

- Status: On Schedule

Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$6,624,137
