

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

April 17, 2020



**Prepared For:** Atlanta Public Schools

**Prepared By:** Tony Washington



Main Building Exterior Paint




Asphalt Paving at Auto/Aviation Lab Drive



VCT Flooring at Graphics Lab 252



Carpet at Classroom 243

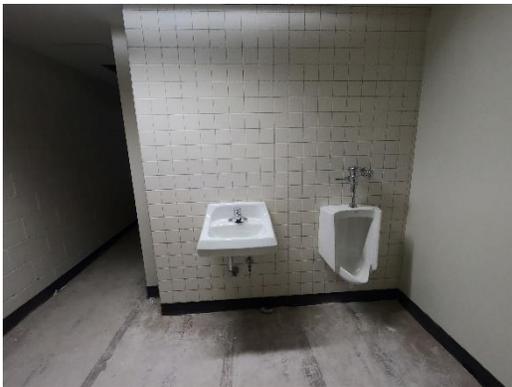

First Floor Restroom Plumbing Fixtures



Automotive Lab Sealed Concrete Flooring Prep.

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

April 17, 2020



### Last Week's Activities:

- Continued sealed concrete flooring installation at first floor
- Completed epoxy wall paint at Cafeteria Kitchen
- Continued exterior paint at main building
- Continue installation of vertical fan coil units
- Continued ceiling grid installation
- Continued installation of plumbing fixtures at first floor
- Continued installation of exterior curbs and flatwork
- Completed painting of exposed ceiling at second floor commons
- Continued sprinkler head drop at first floor
- Began installation of VCT flooring at second floor

### This Week's Activities:

- Continued sealed concrete flooring installation at first floor
- Completed concrete pour back for riser
- Continue exterior paint at main building
- Began installation of toilet partitions at second floor
- Continued ceiling grid installation
- Continued installation of plumbing fixtures at restrooms
- Continued installation of VCT flooring at second floor
- Began installation of carpet at second floor
- Continue sprinkler head drop at first floor
- Began asphalt paving at Auto/Aviation Lab drive
- Began sealed concrete floor prep at Auto/Aviation Labs
- Completed installation of grease duct at Cafeteria Kitchen

### Next Week's Activities:

- Continue sealed concrete flooring installation at first floor
- Began sealed concrete floor prep at Auto/Aviation Labs
- Continue installation of toilet partitions at second floor
- Continue ceiling grid installation
- Continue installation of plumbing fixtures at restrooms
- Continue installation of VCT flooring at second floor
- Continue sprinkler head drop at first floor
- Continue carpet installation at second floor
- Begin site straw and seeding
- Continue installation of electrical devices

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

April 17, 2020



### Schedule:

- Status: On Schedule

### Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$6,624,137
