

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

April 24, 2020




**Prepared For:** Atlanta Public Schools

**Prepared By:** Tony Washington



Car Lifts Installed at Automotive Lab

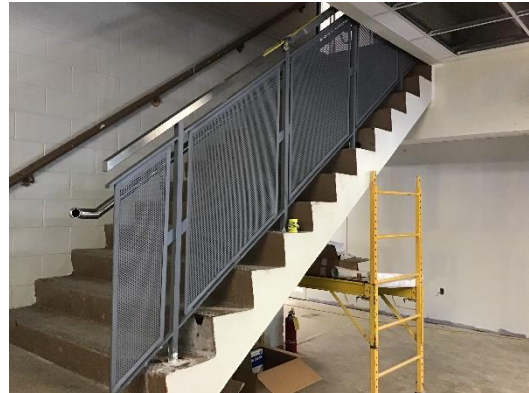

Handrail Installation Ongoing at Main Stairs



Metal Canopy Installed



Light Fixtures Installed at Nursing Lab 129



New Fire Riser at Building Storage Room 135



Wood Doors on Site

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

April 24, 2020



### Last Week's Activities:

- Continued sealed concrete flooring installation at first floor
- Completed concrete pour back for riser
- Began installation of toilet partitions at second floor
- Continued ceiling grid installation
- Continued installation of plumbing fixtures at restrooms
- Continued installation of VCT flooring at second floor
- Began installation of carpet at second floor
- Continue sprinkler head drop at first floor
- Began asphalt paving at Auto/Aviation Lab drive
- Began sealed concrete floor prep at Auto/Aviation Labs
- Completed installation of grease duct at Cafeteria Kitchen

### This Week's Activities:

- Continued sealed concrete flooring installation at first floor
- Completed concrete pour back for riser
- Continued ceiling grid installation
- Completed installation of plumbing fixtures at restrooms
- Continued sprinkler head drop at first floor
- Completed ceiling grid installation at Cafeteria Kitchen
- Completed installation of light fixtures at Cafeteria Kitchen
- Automotive Lab car lifts installation by APS is complete
- Began installation of wood doors

### Next Week's Activities:

- Continue sealed concrete flooring installation at first floor
- Begin installation of light fixtures at second floor Commons 201
- Begin floor leveling at Aviation Lab
- Begin ceiling tile installation at Cafeteria Kitchen
- Continue installation of VCT flooring at second floor
- Continue sprinkler head drop at first floor
- Continue installation of electrical devices
- Continue installation of wood doors
- Complete installation of sectional door at Aviation Lab

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

April 24, 2020



### Schedule:

- Status: On Schedule

### Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$7,339,365
