

**WEEKLY CONSTRUCTION PROGRESS
REPORT**
Atlanta College and Career Academy
May 01, 2020



Prepared For: Atlanta Public Schools


Prepared By: Tony Washington




Light Fixtures Installed at Automotive Lab



Pipe Grid Installation Ongoing at Aviation Lab

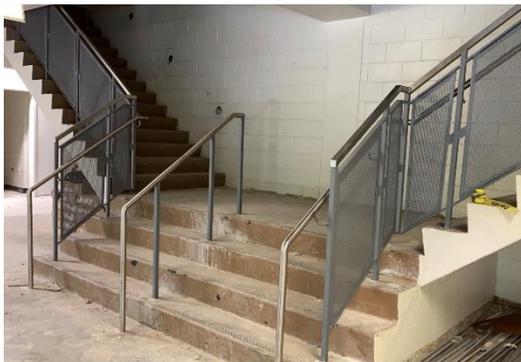

Handrail Installation Ongoing at Main Stairs

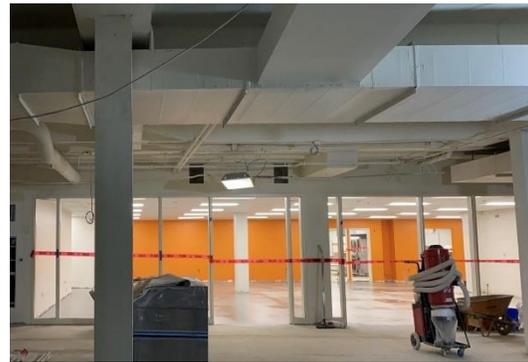

Exposed Ceiling Painted at Commons 156



Carpet Installed at Media Center 261



Carpet Installed at Second Floor Corridor

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

May 01, 2020



Last Week's Activities:

- Continued sealed concrete flooring installation at first floor
- Completed concrete pour back for riser
- Continued ceiling grid installation
- Completed installation of plumbing fixtures at restrooms
- Continued sprinkler head drop at first floor
- Completed ceiling grid installation at Cafeteria Kitchen
- Completed installation of light fixtures at Cafeteria Kitchen
- Automotive Lab car lifts installation by APS is complete
- Began installation of wood doors

This Week's Activities:

- Continue sealed concrete flooring installation at first floor
- Began installation of light fixtures at second floor Commons 201
- Began floor leveling at Aviation Lab
- Began ceiling tile installation at Cafeteria Kitchen
- Continued installation of VCT flooring at second floor
- Completed sprinkler head drop at first floor
- Continued installation of electrical devices
- Continued installation of doors and door hardware
- Continued final coat of paint at first floor
- Continued installation of steel handrails at main stairs
- Continued installation of carpet at second floor
- Completed installation of light fixtures at Auto/Aviation Labs
- Completed installation of electrical panels at Auto/Aviation Labs
- Completed painting of exposed ceiling at Commons 156
- Began installation of metal pipe grid at Aviation Lab
- Completed installation of sectional door at Aviation Lab

Next Week's Activities:

- Continue sealed concrete flooring installation at first floor
- Continue sealed concrete floor prep at Aviation Lab
- Continue installation of electrical devices
- Continue installation of doors and door hardware
- Continue final coat of paint at first floor
- Begin installation of UDS at Cafeteria kitchen
- Continue installation of steel handrail at main stairs
- Continue installation of carpet at second floor
- Pour concrete pad for new generator
- Begin installation of monument sign
- Continue installation of metal pipe grid at Aviation Lab

WEEKLY CONSTRUCTION PROGRESS REPORT

Atlanta College and Career Academy

May 01, 2020



Schedule:

- Status: On Schedule

Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$8,839,007
