

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

July 10th, 2020



**Prepared For:** Atlanta Public Schools

**Prepared By:** Tommy Pease



Installation of Auto Equipment in the Automotive Lab 166




Installation of Furniture in the IT Lab 222



Installation of Sinks and FRP Panels in the Culinary Arts Lab 136



Installation of the Casework and Countertops in the Reception 104

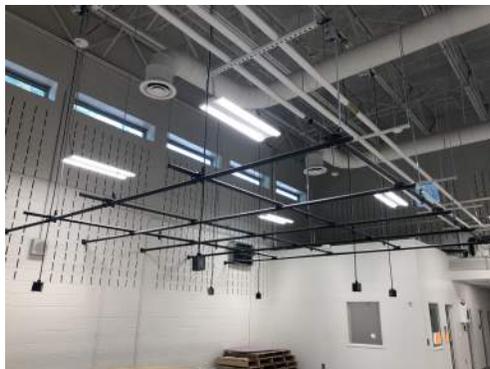

Installation of the Pipe Grid and Drop Down Electrical Outlets in the Aviation Lab 170



Installation of Kitchen Equipment in the Nutrition Kitchen 136

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

July 10th, 2020



### Last Week's Activities:

- Continued installation of doors and door hardware
- Continued kitchen equipment connections in the Culinary Arts Lab
- Continued installation of Ansul systems in kitchen hoods
- Continued HVAC startup
- Continued final cleaning
- Completed testing fire alarm system

### This Week's Activities:

- Continued installation of doors and door hardware
- Continued kitchen equipment connections in the Culinary Arts Lab
- Continued final cleaning
- Completed installation of Ansul systems in kitchen hoods
- Continued HVAC startup
- Received plumbing final inspection

### Next Week's Activities:

- Continue kitchen equipment connections in the Culinary Arts Lab
- Continue final cleaning
- Complete installation of doors and door hardware
- Complete HVAC startup

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Atlanta College and Career Academy

July 10th, 2020



### Budget:

- Construction Budget: \$10,400,000
- Budget Status: On Budget
- Gross Billed to Date: \$8,971,147
