

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Humphries Elementary School

January 10, 2020

**Prepared For:** Atlanta Public Schools

**Prepared By:** Tony Washington



Level 2 Drywall Completion




Storefront Window Frame Installation



Level 2 Ceiling Grid Installation



Exterior Masonry Brick

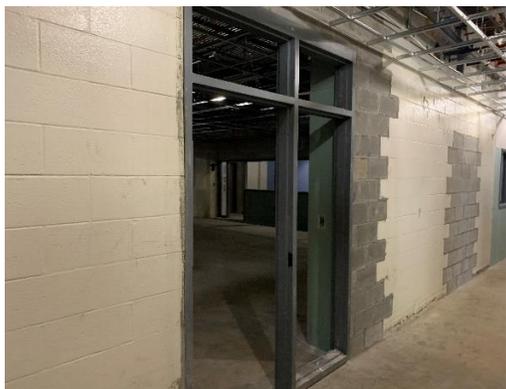

Interior Door Frame Installation



Interior CMU Block Fill in Progress

# WEEKLY CONSTRUCTION PROGRESS REPORT

## Humphries Elementary School

January 10, 2020



### Last Week's Activities:

- Began interior HI drywall installation at building 2030
- Completed in wall MEP rough in at new addition
- Began west brick installation at new addition
- Continued storefront installation at new addition
- Completed canopy foundations

### This Week's Activities:

- Poured courtyard slab on grade
- Continued west brick installation at new addition
- Continued storefront installation at new addition
- Completed level 02 MEP rough in at new addition
- Continued level 02 ductwork installation at new addition
- Continued HVAC start up at building 2032
- Began priming & painting at building 2032
- Continued ceiling framing repairs at buildings 2030 & 2040
- Continued sprinkler system installation at building 2031
- Continued window framing work at building 2031

### Next Week's Activities:

- Complete east elevation hardscapes
- Complete curb & gutter installation
- Complete west brick installation at new addition
- Complete storefront installation at new addition
- Begin east brick at new addition
- Complete building dry in at building 2030
- Complete priming & painting at building 2032
- Begin reinstalling VRFs at buildings 2033 & 2040
- Begin installing ceiling lights at buildings 2033 and 2040
- Continued window framing work at building 2031

### Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

### Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,957,883
