



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 01.01.2021

### THIS WEEK

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Area 1 & 2
- Wall primer install continuing in Area 1 & 2
- Fire suppression continuing in Area 2 & 4
- Roofing continuing in Area 2
- Door frame installation continuing
- Media center structural steel install continuing
- Slab Preparation continuing
- New Year's break 11.31 through 01.03

### NEXT WEEK: 01.04.21 – 01.08.21

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Area 1 & 2
- Wall primer install continuing in Area 1 & 2
- Fire suppression continuing in Area 2 & 3
- Roofing continuing in Area 2
- Door frame installation continuing
- Media center structural steel install continuing
- Placing slab on grade for new gymnasium

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status

\$2,204,953.25

Completed By:  
Chris Hubbard

**PARRISH**  
CONSTRUCTION GROUP

# Photo Updates


## Slab preparation



## Area 2 Roofing



## SOG Vapor barrier install

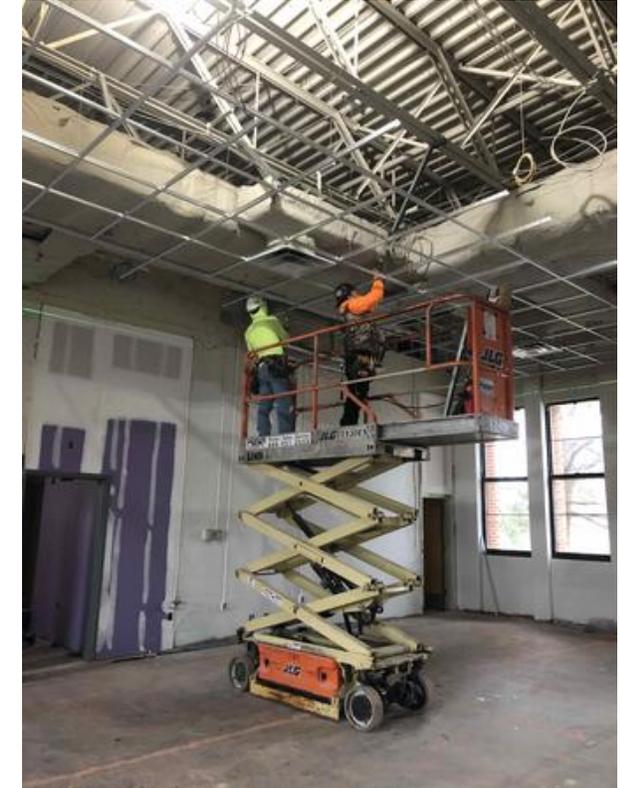

## Ceiling grid install

