



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 01.08.2021

THIS WEEK

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Area 1 & 2
- Painting in Areas 1 and 2
- Fire suppression continuing in Area 2, 3 & 4
- Roofing continuing in Area 2
- Concrete slab for new gym placement
- Ceiling grid install continues in Area 1
- New gymnasium CMU Wall installation beginning

NEXT WEEK: 01.11.21 – 01.15.21

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Area 1 & 2
- Painting continuing in Areas 1 and 2
- Fire suppression continuing in Area 2,3 & 4
- Roofing continuing in Area 2
- Media center structural steel install continuing
- Ceiling grid install continues in Area 1 and beginning in Area 2
- New gymnasium CMU Wall installation continuing

BUDGET

Construction Budget

\$10,900,000.00

Budget Status


\$3,537,864.63

Completed By:
Chris Hubbard

PARRISH
CONSTRUCTION GROUP


Photo Updates

Concrete slab pour

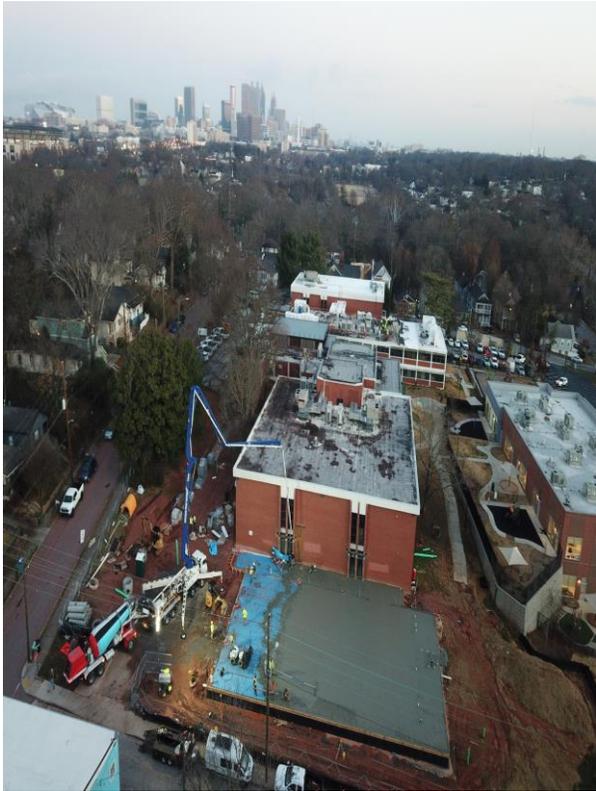

Cloud ceiling
soffit

Hallway Painting

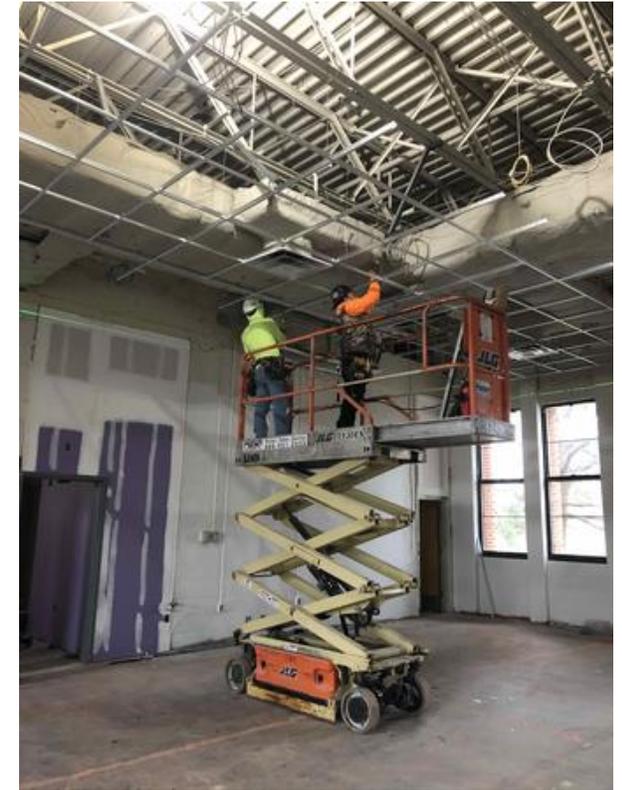

Ceiling grid install

