



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 01.15.2021

### THIS WEEK

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Area 2, 3 & 4
- Painting in Areas 1 and 2
- Fire suppression continuing in Area 2, 3 & 4
- Roofing continuing in Area 2
- Ceiling grid install continues in Area 1 and Area 2
- New gymnasium CMU wall installation continuing
- Door frame installation in new gymnasium begins
- EIFs installation in Area 1

### NEXT WEEK: 01.18.21 – 01.22.21

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Area 2, 3 & 4
- Painting continuing in Areas 1, 2 & 3
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2
- Ceiling grid install continues in Area 1 and Area 2
- New gymnasium CMU wall installation continuing
- Door frame installation in new gymnasium continuing

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status

\$3,537,864.63

Completed By:  
Chris Hubbard

**PARRISH**  
CONSTRUCTION GROUP


# Photo Updates

CMU wall  
installation



Door frame  
installation at  
new gym

EIFs Installation

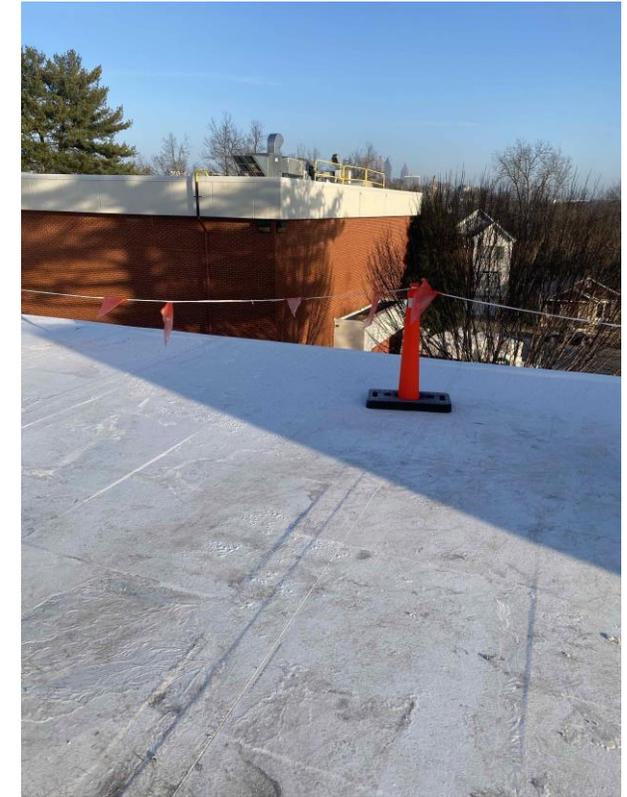

Roofing in Area 2

