



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 01.22.2021

THIS WEEK

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Area 2, 3 & 4
- Painting continuing in Areas 1, 2 & 3
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2
- Ceiling grid install continues in Area 1, 2 & 3
- New gymnasium CMU wall installation continuing
- Door frame installation in new gymnasium continuing
- Fire caulk installation in Area 3 & 4
- Structural Steel erection in new gymnasium

NEXT WEEK: 01.25.21 – 01.29.21

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Area 2, 3 & 4
- Painting continuing in Areas 1, 2 & 3
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2
- Ceiling grid install continues in Area 1, 2 and 3.
- New gymnasium CMU wall installation continuing
- Door frame installation in new gymnasium continuing
- Fire caulk installation continuing in Area 3 & 4

BUDGET

Construction Budget

\$10,900,000.00

Budget Status

\$3,537,864.63

Completed By:
Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo Updates


Fire caulking



Structural steel at new gym



CMU wall at new Gym continues

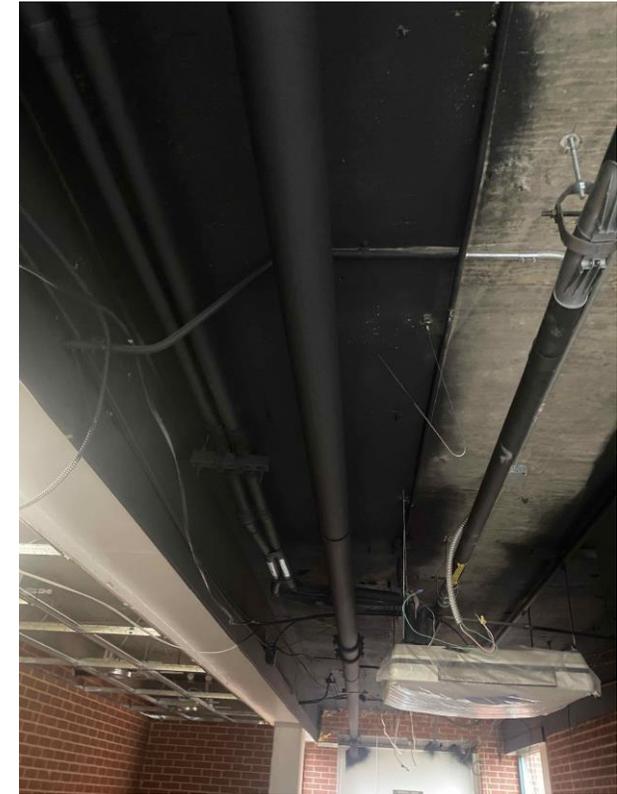

Painting for floating ceiling

