



# Weekly Construction Progress Report

## Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 02.05.2021

### THIS WEEK

- Electrical and plumbing rough-in continuing in Area 3 & 4.
- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Areas 3 & 4
- Painting continuing in Areas 2, 3 & 4
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2, 3 & 4
- Ceiling grid install continues in Area 3 & 4
- New gymnasium CMU wall installation continuing
- Ceiling tile installation in Area 1 continues
- Light fixture install in Area 1

### NEXT WEEK: 02.08.21 – 02.12.21

- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Areas 3 & 4
- Painting continuing in Areas 3 & 4
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2, 3 & 4
- Ceiling grid install continues in Area 3 & 4
- New gymnasium CMU wall installation continuing
- Door frame painting continues in Area 1
- Ceiling Tile installation continuing in Area 1 and beginning in Area 2
- Light fixture installation continues in Area 1 & beginning in Area 2
- Epoxy flooring installation in restrooms

### BUDGET

#### Construction Budget

\$10,900,000.00

#### Budget Status

\$4,860,760.45

Completed By:  
Chris Hubbard


**PARRISH**  
CONSTRUCTION GROUP

# Photo Updates

Light fixture install



Demolition for  
Wheelchair  
Ramp

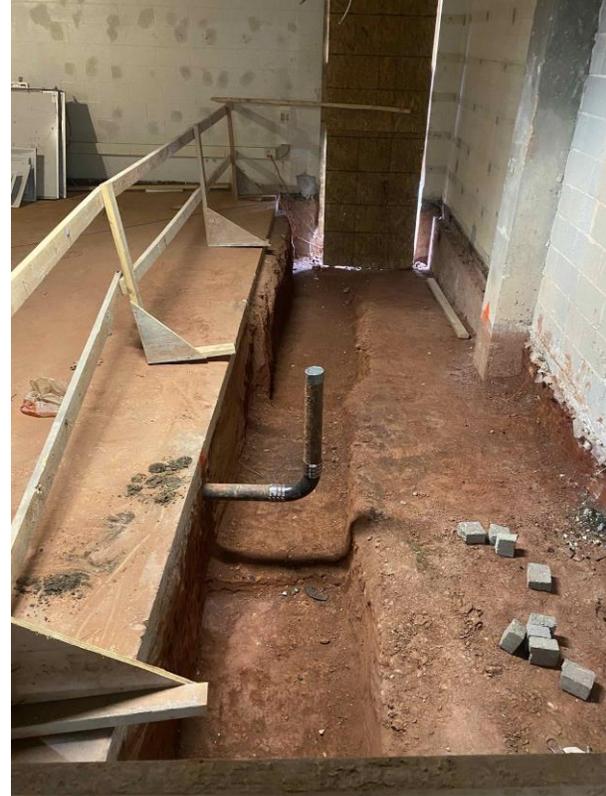

Concrete  
demolition



Sheathing at  
security vestibule

