



Weekly Construction Progress Report

Addition and Renovation work to Barack & Michelle Obama Academy

Week Ending: 02.19.2021

THIS WEEK

- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Areas 3 & 4
- Painting continuing in Areas 3 & 4
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2, 3 & 4
- Ceiling grid install continues in Area 3 & 4
- New gymnasium CMU wall installation continuing
- Ceiling tile installation continues in Area 1 & 2
- Light fixture installation continues in Area 1 & 2
- Handicap ramp installation continues in Area 4
- Fixed seating installation continues
- Bar joist installation continues

NEXT WEEK: 02.22.21 – 02.26.21

- HVAC relocation continuing
- Drywall installation continuing
- Drywall finishing continuing in Areas 3 & 4
- Painting continuing in Areas 3 & 4
- Fire suppression continuing in Area 3 & 4
- Roofing continuing in Area 2, 3 & 4
- Ceiling grid install continues in Area 3 & 4
- New gymnasium CMU wall installation continuing
- Ceiling Tile installation continues in Area 1 & 2
- Light fixture installation continues in Area 1 & 2
- Handicap ramp installation continues in Area 4
- Fixed seating installation continues
- Fireproofing begins
- Bar joist installation continues
- Roof deck installation begins at new gym

BUDGET

Construction Budget

\$10,900,000.00

Budget Status


\$4,860,760.45

Completed By:
Ben Fairchild


PARRISH
CONSTRUCTION GROUP

Photo Updates

CMU wall at media center

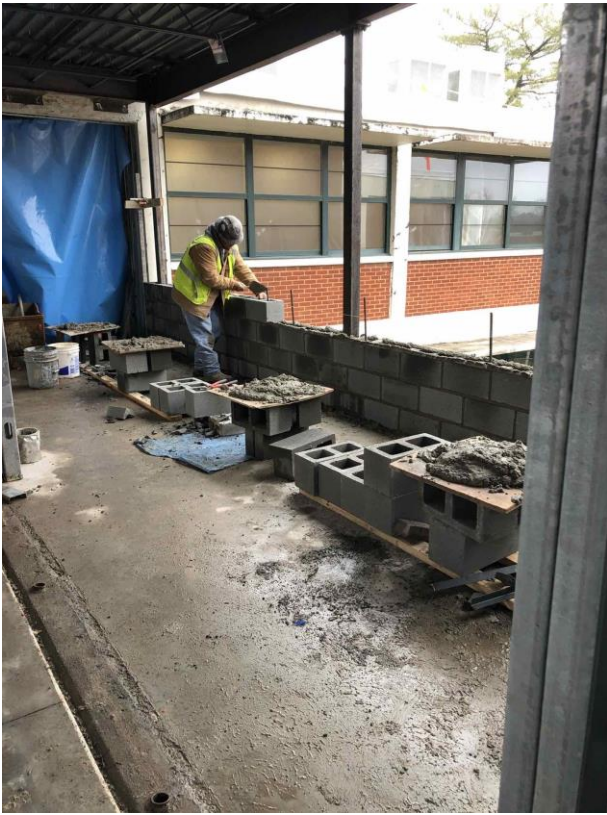

HVAC unit installation

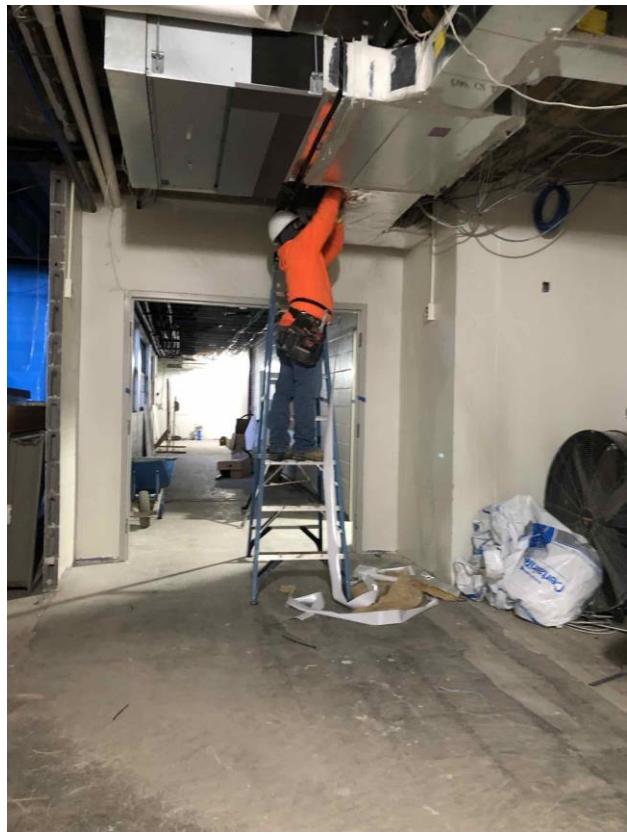

Bar joist installation at new gym



Light fixture installation

